



VILLA NO. 05 MODEL VILLA EXTERNAL PLASTERING WORK IN PROGRESS.



VILLA NO. 18 FIRST FLOOR COLUMN REINFORCEMENT WORK IN PROGRESS.



VILLA NO. 09 G.F ROOF SLAB CONCRETE WORK COMPLETED.



VILLA NO. 45 G.F ROOF SLAB COMPLETED.



VILLA NO. 72 G.F ROOF SLAB REINFORCEMENT WORK IN PROGRESS.



VILLA NO. 07 TWO LINE BLOCK WORK COMPLETED.



VILLA NO. 06 LIFT PIT COLUMN SHUTTERING WORK IN PROGRESS.



VILLA NO. 70 G.F COLUMN COMPLETED.



VILLA NO. 46 G.F COLUMN SHUTTERING WORK COMPLETED.



VILLA NO. 12 SOIL BACKFILLING WORK UP TO PLINTH BEAM IS COMPLETED .



VILLA NO. 66 PLINTH BEAM COMPLETED.



VILLA NO.10 PLINTH BEAM COMPLETED.



VILLA NO. 50 PLINTH BEAM DE-SHUTTERING WORK IN PROGRESS.



VILLA NO. 65 PLINTH BEAM REINFORCEMENT & SHUTTERING WORK COMPLETED.




VILLA NO. 14 PLINTH BEAM SHUTTERING WORK IN PROGRESS.



VILLA NO. 47 PLINTH BEAM REINFORCEMENT & SHUTTERING WORK IN PROGRESS.



VILLA NO. 15 PLINTH BEAM REINFORCEMENT WORK IN PROGRESS.

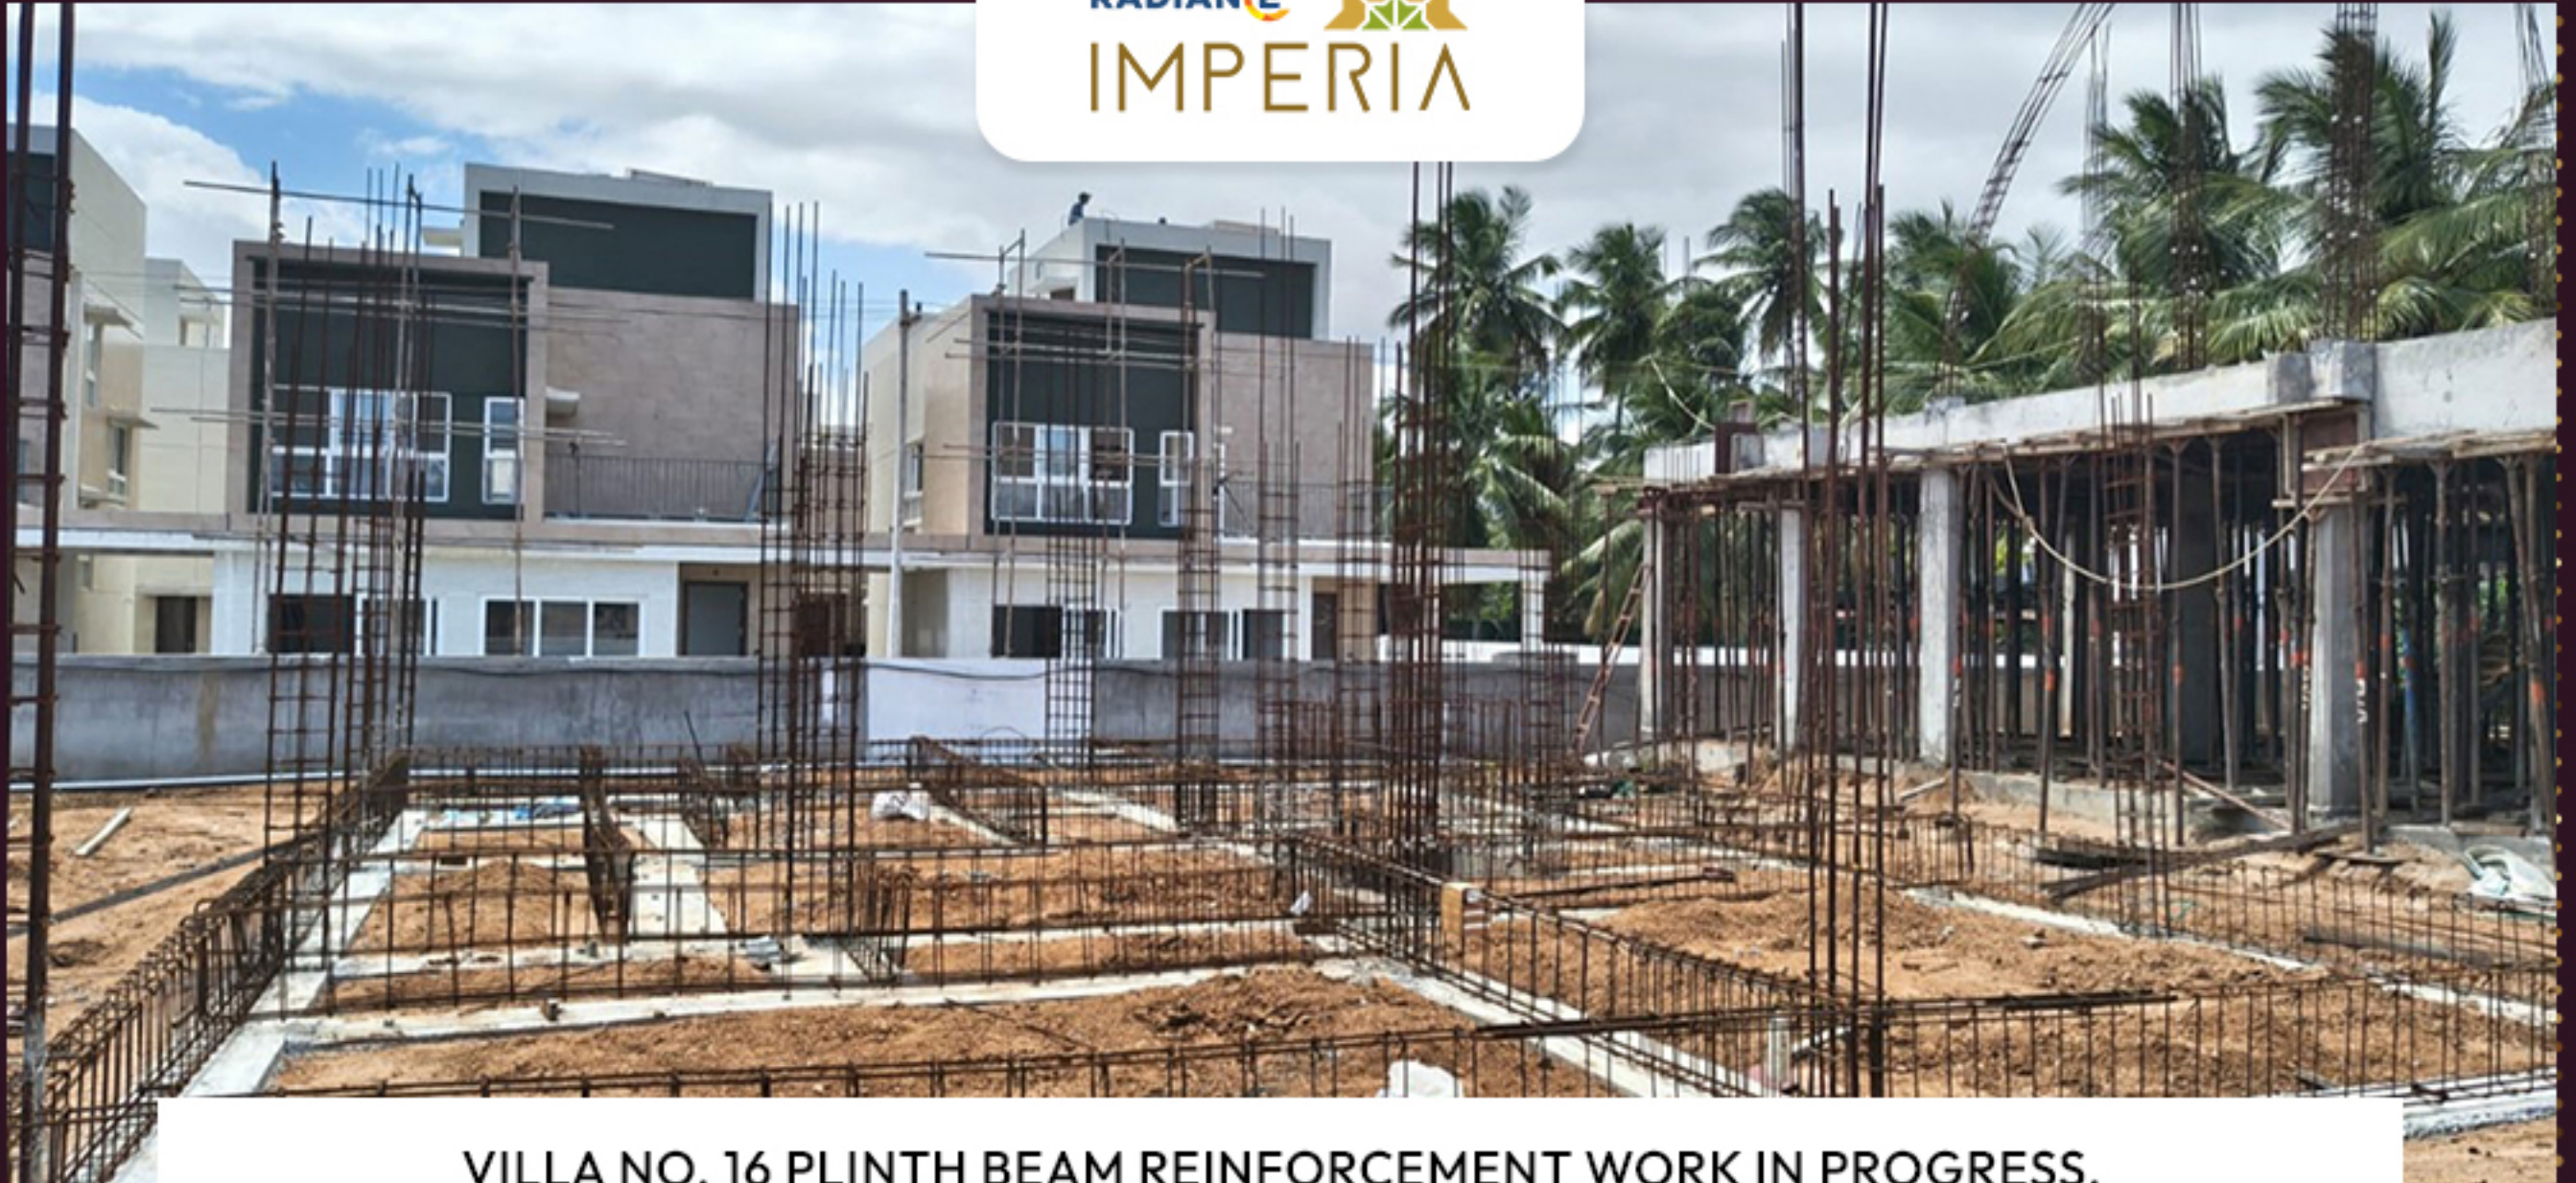

VILLA NO. 16 PLINTH BEAM REINFORCEMENT WORK IN PROGRESS.



VILLA NO. 69 PLINTH BEAM PCC COMPLETED.



VILLA NO. 51 PLINTH BEAM PCC COMPLETED.



VILLA NO. 11 PLINTH BEAM PCC FORM WORK COMPLETED.



VILLA NO. 19 SOIL COMPACTION WORK IN PROGRESS UP TO PEDESTAL.



VILLA NO 20. SOIL COMPACTION WORK IN PROGRESS UP TO PEDESTAL.



VILLA NO. 04 LIFT PIT PLASTERING WORK IN PROGRESS.



VILLA NO. 03 PEDESTAL COLUMN COMPLETED.



VILLA NO. 88,90,91,92,93 FOOTING REINFORCEMENT WORK IN PROGRESS.



VILLA NO. 21, 22, 23 FOOTING REINFORCEMENT WORK IN PROGRESS.



VILLA NO. 95,96 & 97 FOOTING PCC WORK COMPLETED.



VILLA NO. 01 & 02 FOOTING PCC FORM WORK IN PROGRESS.



VILLA NO. 81,82,83,84,86,87 EARTHWORK EXCAVATION WORK IN PROGRESS.
