



SOUTH EAST SIDE



Block A – Elevation

West SIDE


SOUTH SIDE



Block A – Elevation



Block A – AAC Block Wall Works In The First To Fourth Floor Level

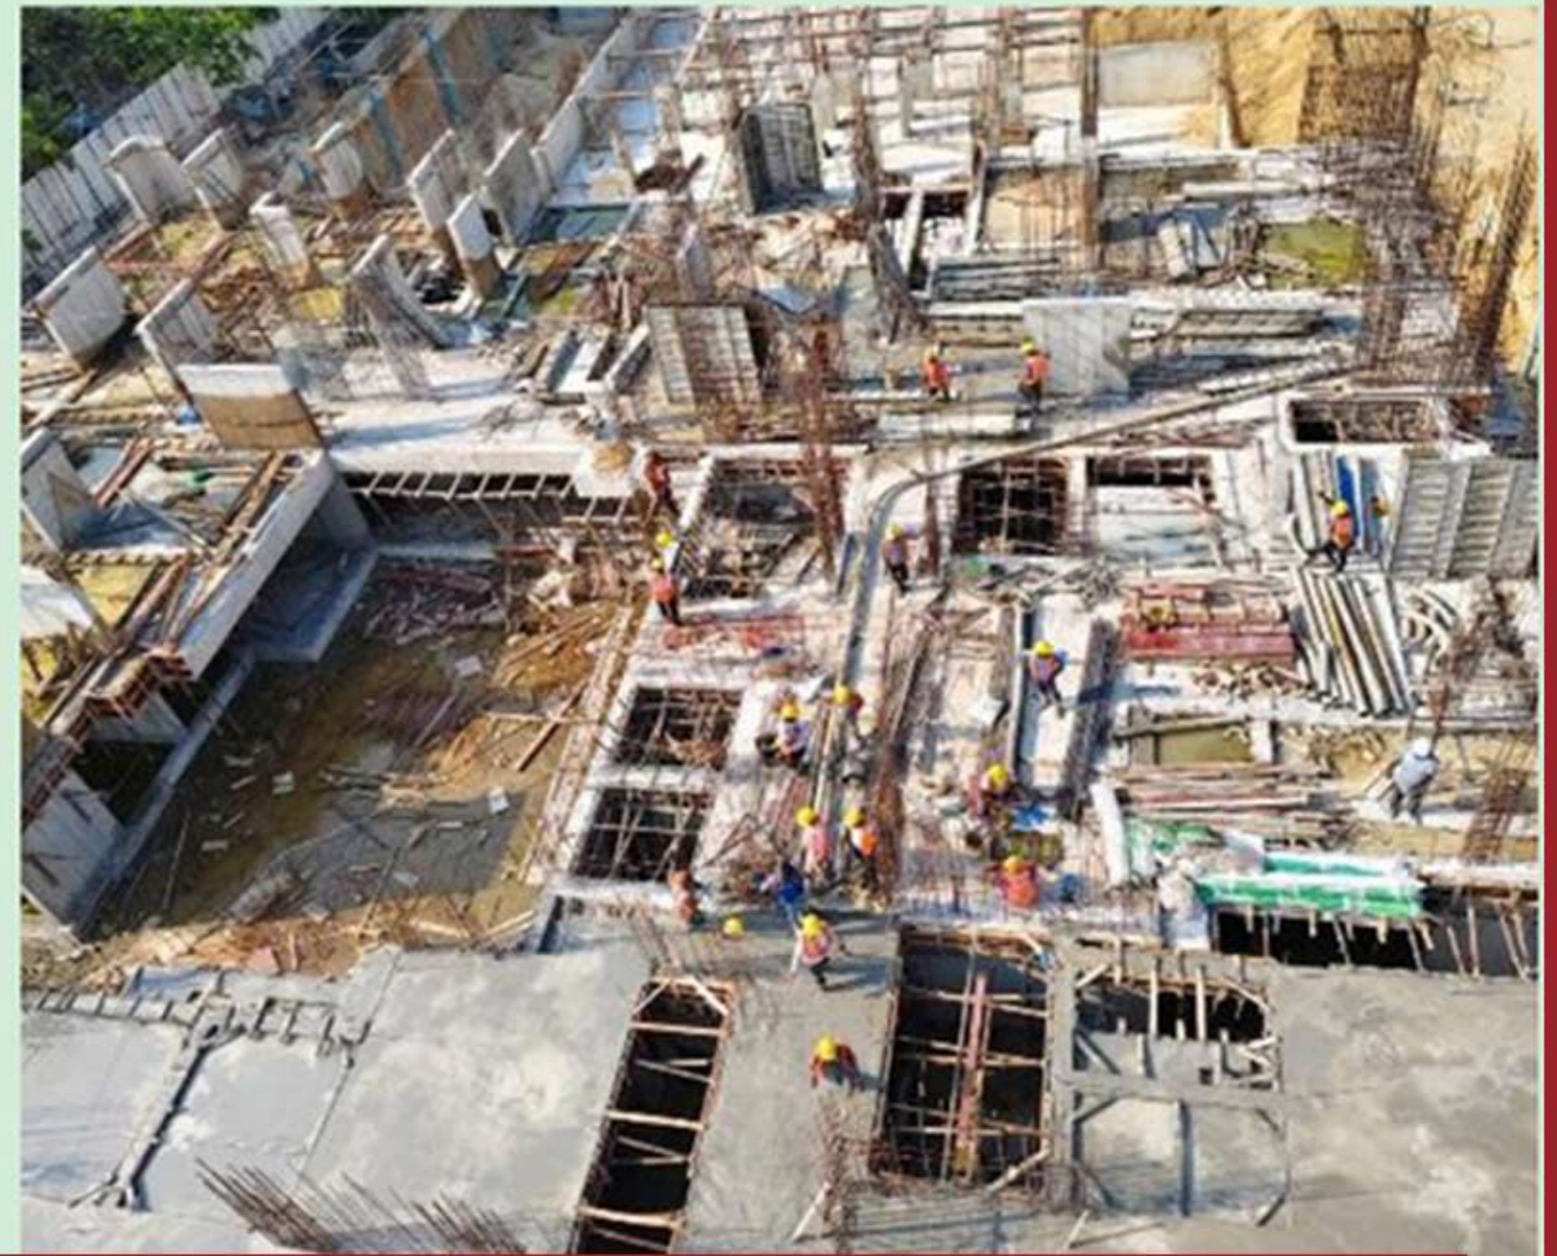

Block B B1 Roof Slab Level / Upper Basement Slab Concrete Works Has Been Completed On 21.2.26 stilt Floor Roof / First Floor Slab Concrete Works Has Been Completed On 01.04.26 1st Floor Roof Level – South And Central Side Slab Concrete Completed & North Side Slab Shuttering

Wip



Block B – Elevation



NORTH EAST SIDE



NORTH WEST SIDE

Block B – Elevation




Block D / Club House –raft-rcc Works Has Been Completed B2 Level - Columns & Retaining Wall Concrete Works Are Completed. and Raft Above Soil Filling Completed & Pcc Wip



Block C – Columns above B2 level

Block C – Raft Concrete Completed On 27.2.26 And Stp – Raft Completed On 18.3.26
Blockc – Columns Works Completcd On 18.4.26 And – Stp B2 Level Retaining Wall Works In Progress

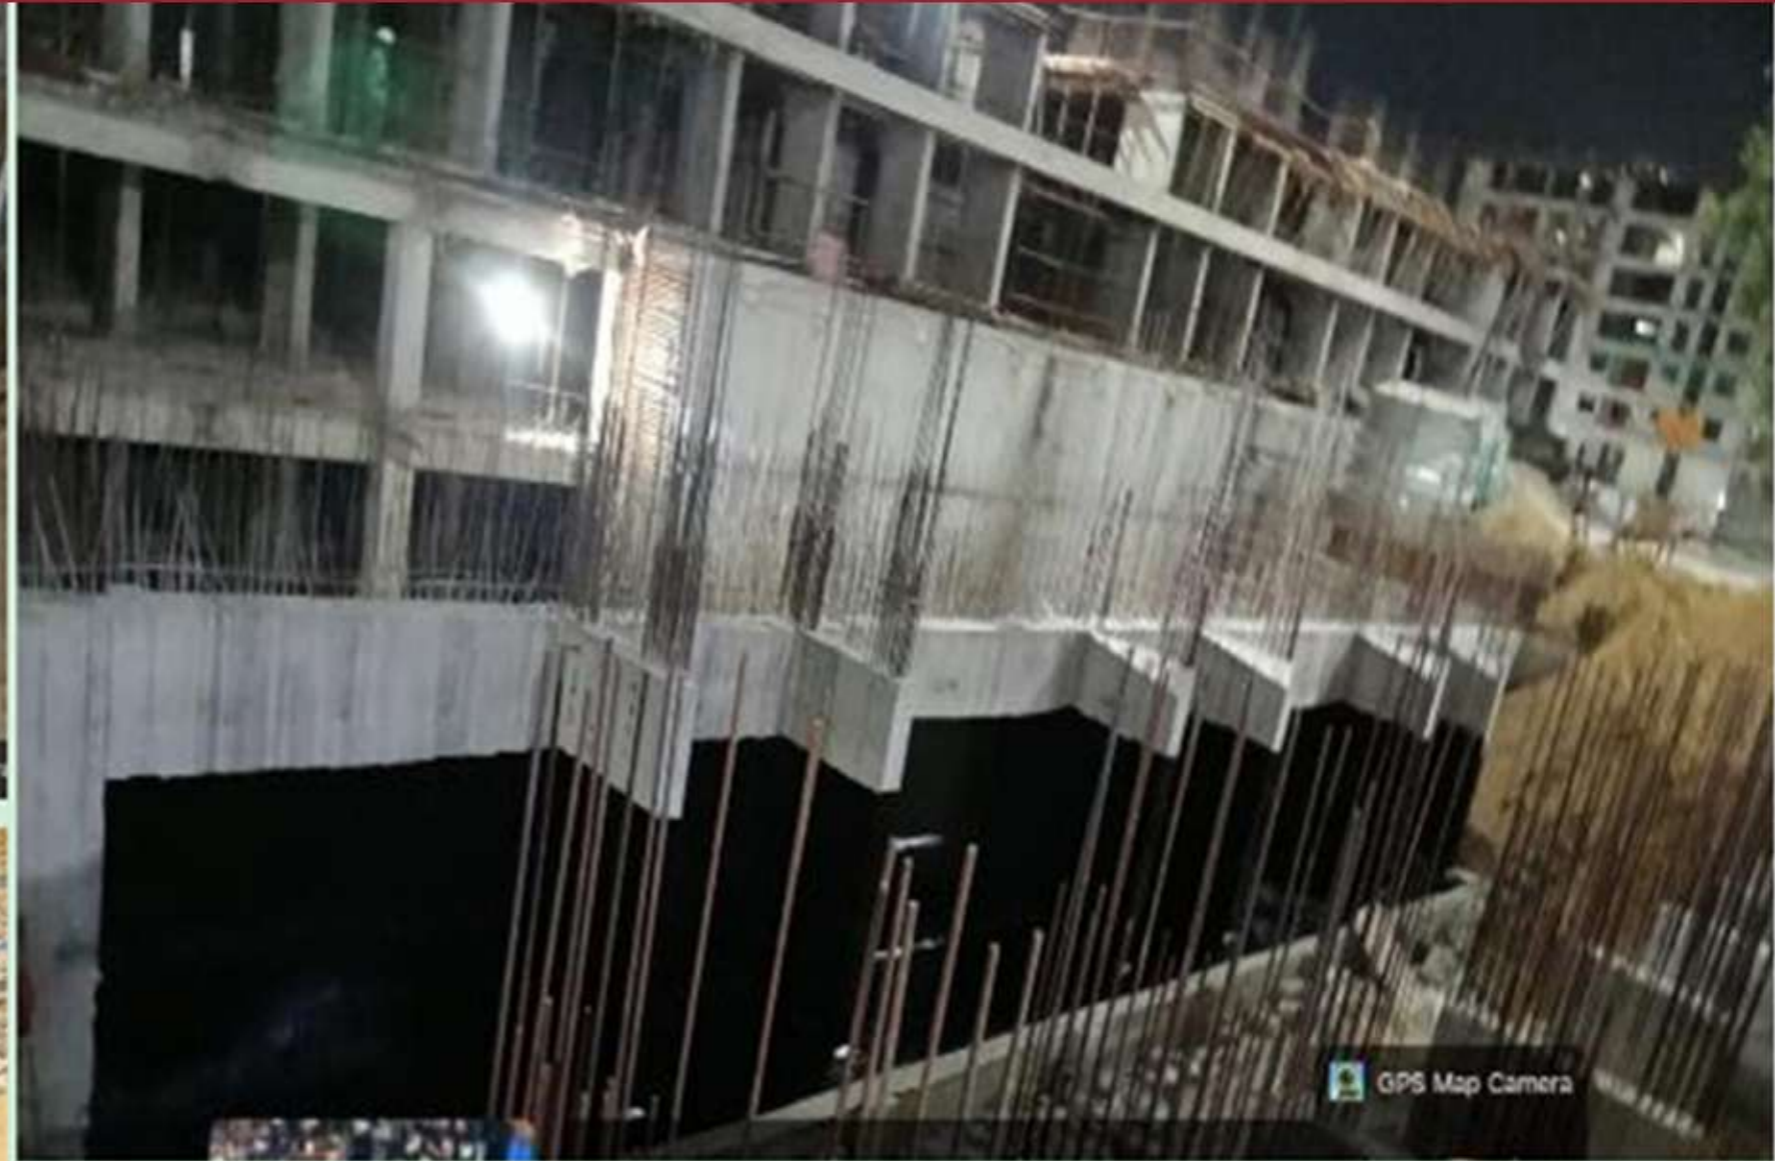

STP - West side retaining wall area, Primer & SBS Membrane laying

STP - Water Proofing And Soil Backfilling Works



Block B, Club House & Block A



Block A –fifth Floor Roof Slab Completed. Sixth Floor Roof Slab Works In Progress. Block B – Stilt Floor Roof Slab Concrete Works Completed & First Floor Roof Slab Works In Progress. Block C - Raft Concrete Works Has Been Completed . Columns & Retaining Wall Works In Progress. Block D / Club House – Raft, B2 Level - Retaining Wall And Columns Concrete Completed. Roof Slab Shuttering Wip

7th floor roof level works



6th floor roof level works



Block A B2 Roof Slab On 10.10.25 , B1 Roof Slab On 15.11.25 And Stilt Roof Slab Completed On 14.12.25 1st Floor Roof Completed On 04.01.26 ,2nd Floor Roof Slab Completed On 25.01.26 , 3rd Floor Roof Slab Completed On 18.2.26, 4th Floor Roof slab Completed On 17.3.26 & 5th Floor Roof Slab Completed On 4.4.26. sixth Floor Roof Slab Level – South Side / Pour 1 (Units 1- 5) & Pour 2 (Units - 6,7,8,14,15 & 16) Slab Concrete Completed and Pour 3 Slab Shuttering (Units 9,10,11,12 & 13) Works In Progress seventh Floor Roof Slab Level – South Side / Pour 1 (Units 1- 5) Slab Shuttering Works In Progress
