




BLOCK A – RAFT RCC COMPLETED IN PART 1 (SW SIDE) & PART 2 (SE SIDE)
COLUMNS & RETAINING WALL CONCRETE WIP.
PART 3 – RAFT CONCRETE WORKS IN PROGRESS (PLANNED QTY 1140CUM)



BLOCK A –LOWER BASEMENT ROOF SLAB LEVEL RETAINING WALL &
COLUMN CONCRETE WORKS COMPLETED / SW SIDE / PART 1




BLOCK A – RAFT PART 2 SOUTH EAST SIDE COLUMN & RETAINING WALL CONCRETE WIP

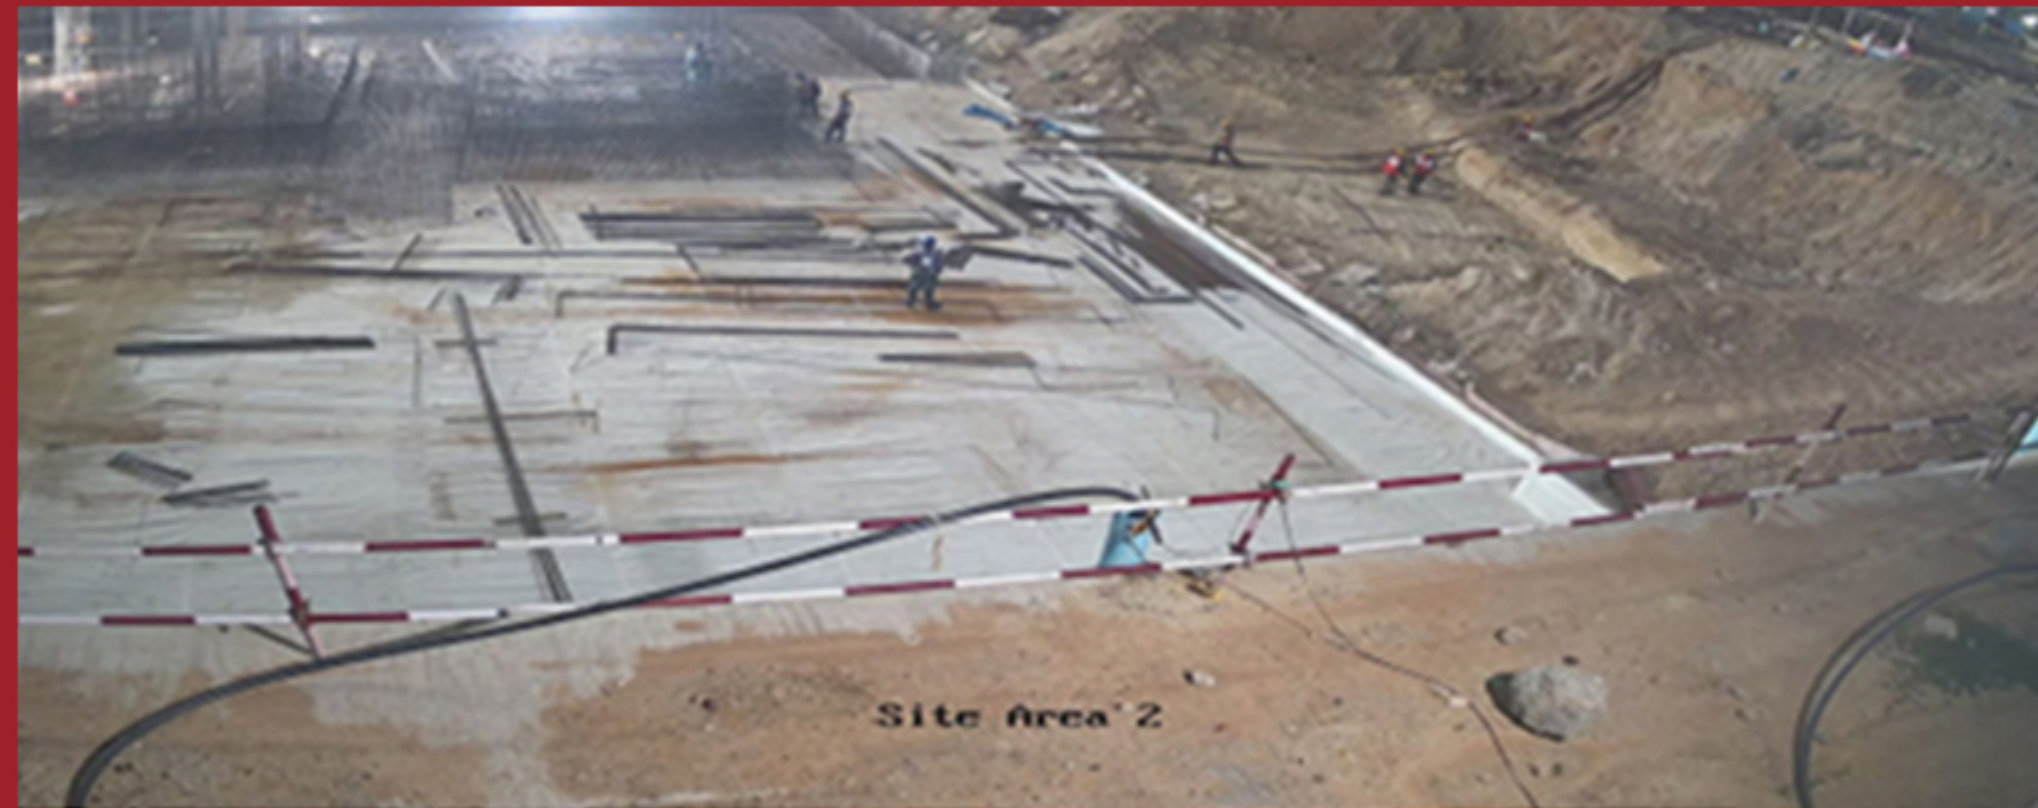

BLOCK A - PART 3 & 4 (TILL CH JUNCTION) WATERPROOFING
COMPLETION AND RAFT REINFORCEMENT WORK



BLOCK A – SOUTH AND EAST SIDE RETAINING WALL WORKS

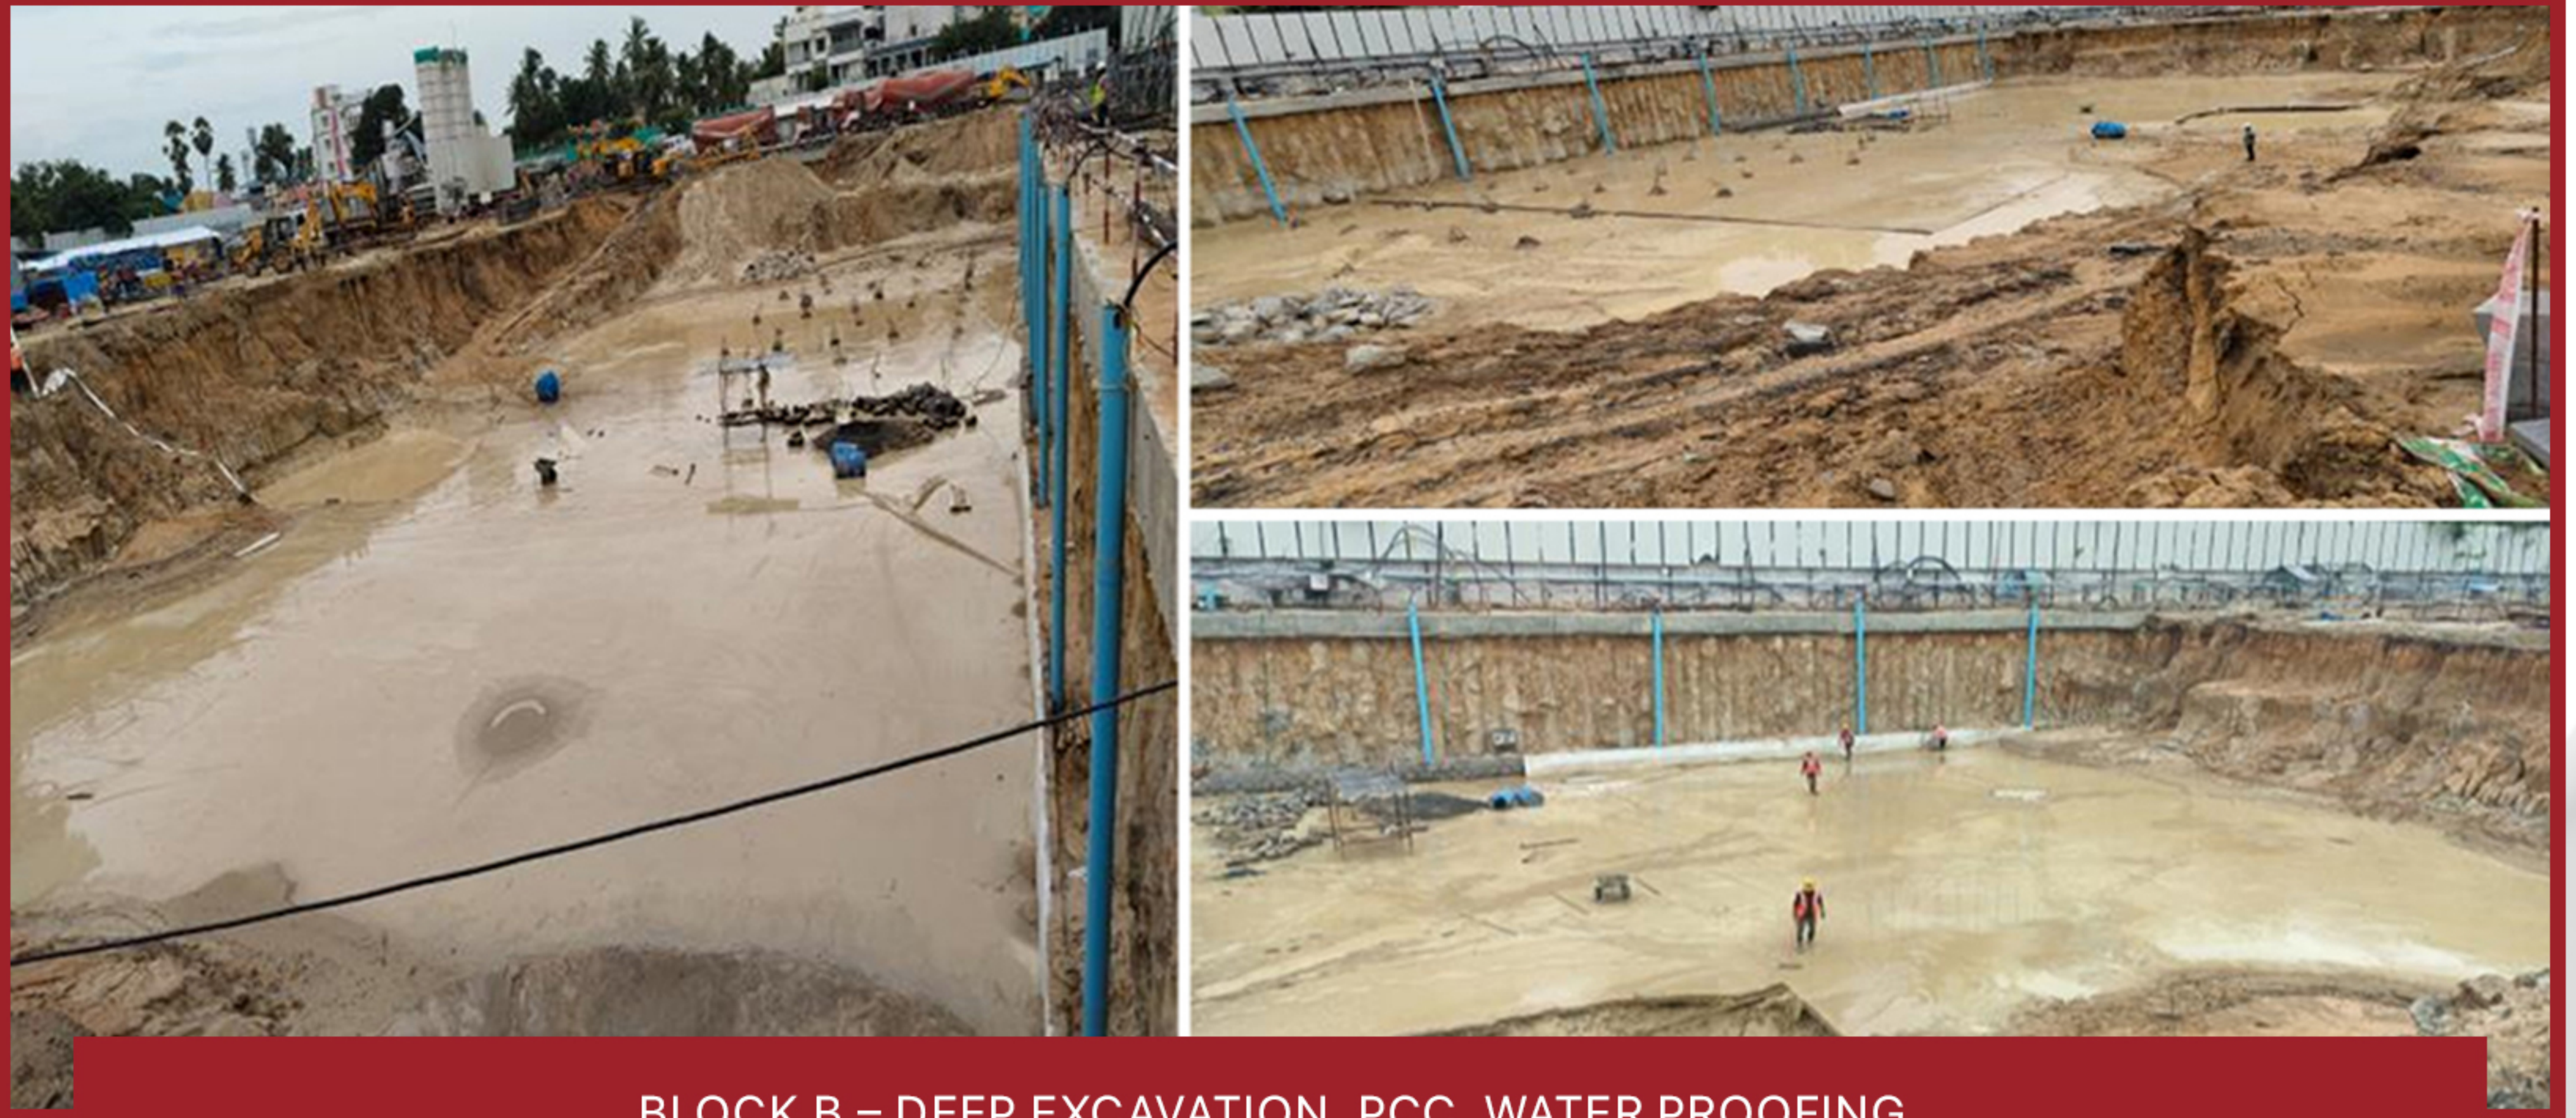

BLOCK B – DEEP EXCAVATION ,PCC, WATER PROOFING,
DEWATERING & SLUSH REMOVING WORKS IN PROGRESS



AN INTENSE CLOUDBURST OVER CHENNAI ON 30.08.2025 NIGHTTIME AND HEAVY RAIN ON 31.8.25 LED TO HEAVY FLOODING AT THE PROJECT SITE. THE PLANNED RAFT RCC FOR BLOCK A/PART 3 AND BLOCK B – EXCAVATION AND RAFT PCC WAS SEVERELY IMPACTED DUE TO WATERLOGGING AND SLUSH ACCUMULATION. IMMEDIATE DEWATERING AND CLEANUP EFFORTS WERE UNDERTAKEN, ENABLING SITE READINESS FOR CONCRETE WORK BY 01.09.2025.
