




External Development : 1. Compound Wall : East Side Retaining Wall 2nd Lift Works Completd At East Side Of Block A , Wtp & Block B.
2. Rainwater Tank At Clubhouse West Side : Raft Foundation And Wall Concrete Completed Till B2 Roof Slab Level

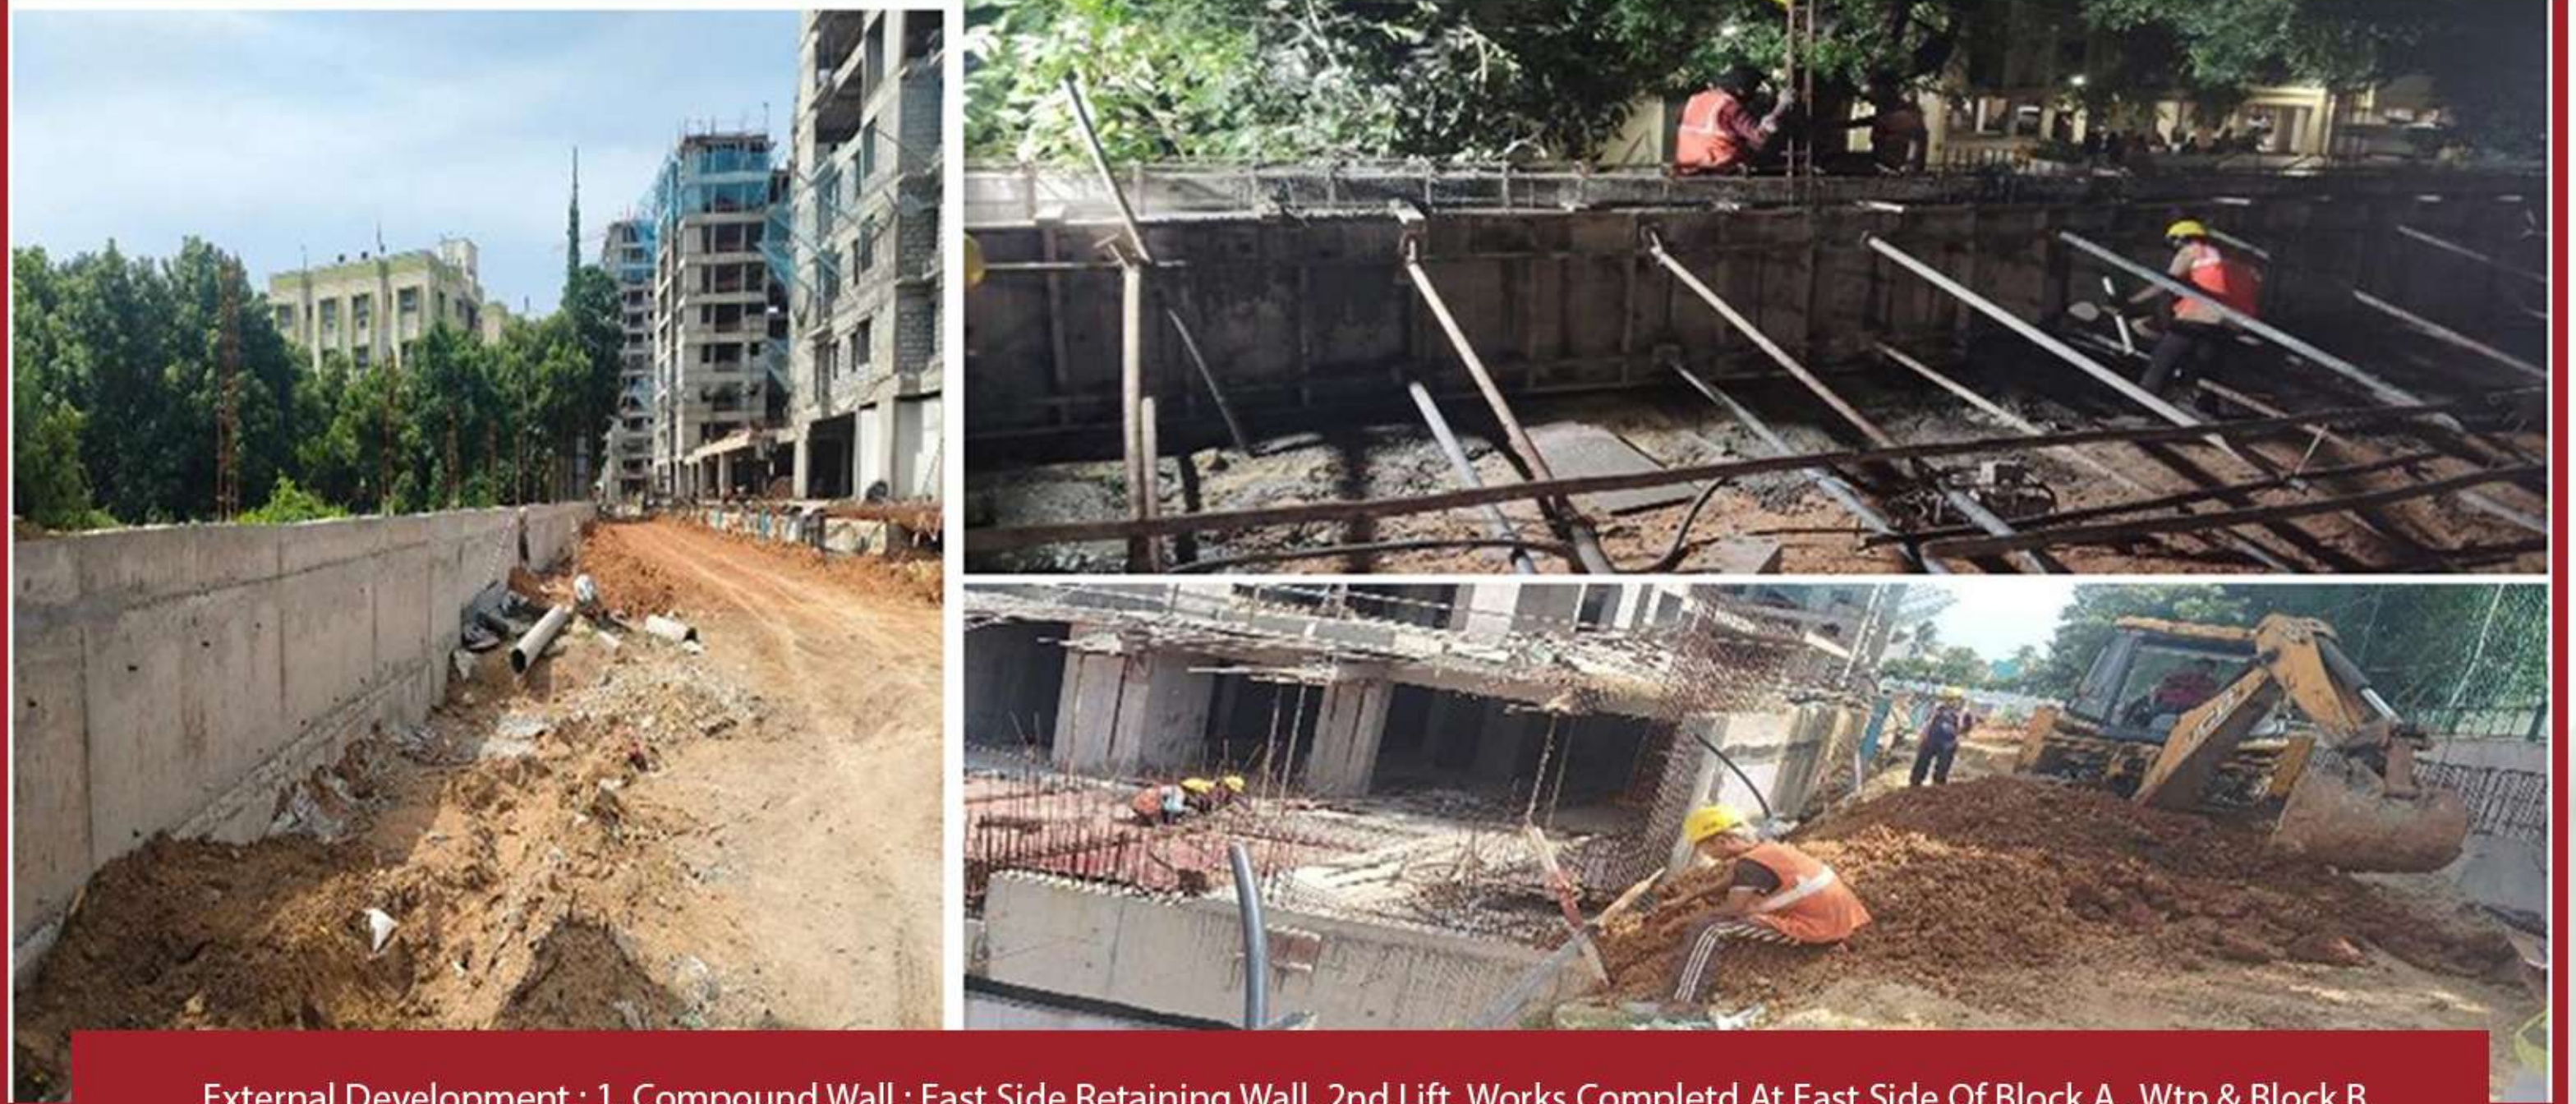

BLOCK - C

Block A – Eleventh Floor Roof Slab Fully Completed. Twelfth & Thirteenth Floor Roof Slab Works In Progress. block B – Seventh Floor Roof Slab Concrete Works Completed. Eighth Floor Roof Slab Works In Progress. block C – Second Floor Roof Slab Works Has Been Completed. Third Floor Roof Slab Works In Progress. block D / Club House – B2 Level - Retaining Wall & Roof Slab Rcc Completed. B1 Level – Columns Works In Progress.



Block D / Club House –b2 Level Columns , Retaining Wall & External Waterproofing Works Completed.b2 Roof Level Slab Concrete Works Completed (Except Shrinkage Strip Area) B1 Level – Columns Works In Progress



Block - A, Block - B & Clubhouse View



Block A :eleventh Floor Roof Slab : Roof Slab Concrete Fully Completed On 10.8.26. Twelfth Floor Roof Slab Pour 1 (Units 1- 5) And Pour 2 (Unit-6,7,8,14,15&16) Concrete Completed Pour 3 –slab Reinforcement Works In Progress. Thirteenth Floor Roof Slab Pour 1 (Units 1- 5) Shuttering Works In Progress.



Block A – Elevation



Block A – East Side Podium Level Elevation



Block A – Elevation



EXTERNAL PLASTERING WORK



Block A – Aac Block Works : Up To 8th Floor Completed. 9th & 10th Wip. Wall Plastering - 1st –4th Floor Cement Plaster Completed. 5 & 6 Th Floor Gypsum Wip. Electrical Wall Chasing ,db Box & Conduit Instalation 1st -5th Floor Completed. 6 & 7th Floor Wip. Phe First Fix : Toilet & Kitchen Plumbing Line Progress In 1 – 4th Floor And Fire Fighting Line Works In Progress.

SOUTH SIDE



NORTH SIDE



Block B : Seventh Floor – Roof Slab Concrete Fully Completed On 28.8.26 Eight Floor Pour 1 (Unit 1-5) Slab Reinforcement Works In Progress And Pour 2 (Unit 6-8 & 14-16) - Column Works In Progress.



Block B – Elevation

TOWARDS SOUTH EAST SIDE



TOWARDS NORTH EAST SIDE



Block B – Elevation / First Floor Podium Level Elevations



Block B – Elevation / First Floor Podium Level Elevations



Block B : 1st – 4th Floor Aac Block Works , Lintel Concrete , Electrical Conduit Works In Progress & 1st Floor Plastering Wip



Block C : Second Floor Roof Slab Level Slab Concrete Completed And 3rd Floor Slab Shuttering & Reinforcement Works In Progress. stp – Inner Retaining Wall And Cover Slab Shuttering & Concrete Works In Progress.



Stp :b1 Lev1 Inner Retaining Wall Works In Progress stilt Floor Slab / Cover Slab & Walkway Slab Concrete Completed At South Side
