



Block A –FOURTH floor roof slab's shuttering AND REINFORCEMENT works in progress.

Block B –BASEMENT SLABS COMPLETED. Stilt floor roof slab works in progress.

Block D / Club house – Raft concrete completed . B2 level - retaining wall AND columns works in progress.




Block B – B2 roof SLAB completed on 10.10.25 and B1 roof slab / stilt floor slab concrete WORKS HAS BEEN completed ON 15.11.25


Stilt roof level / 1st floor slab level slab concrete has been completed on 14.12.25




Block A – External Views

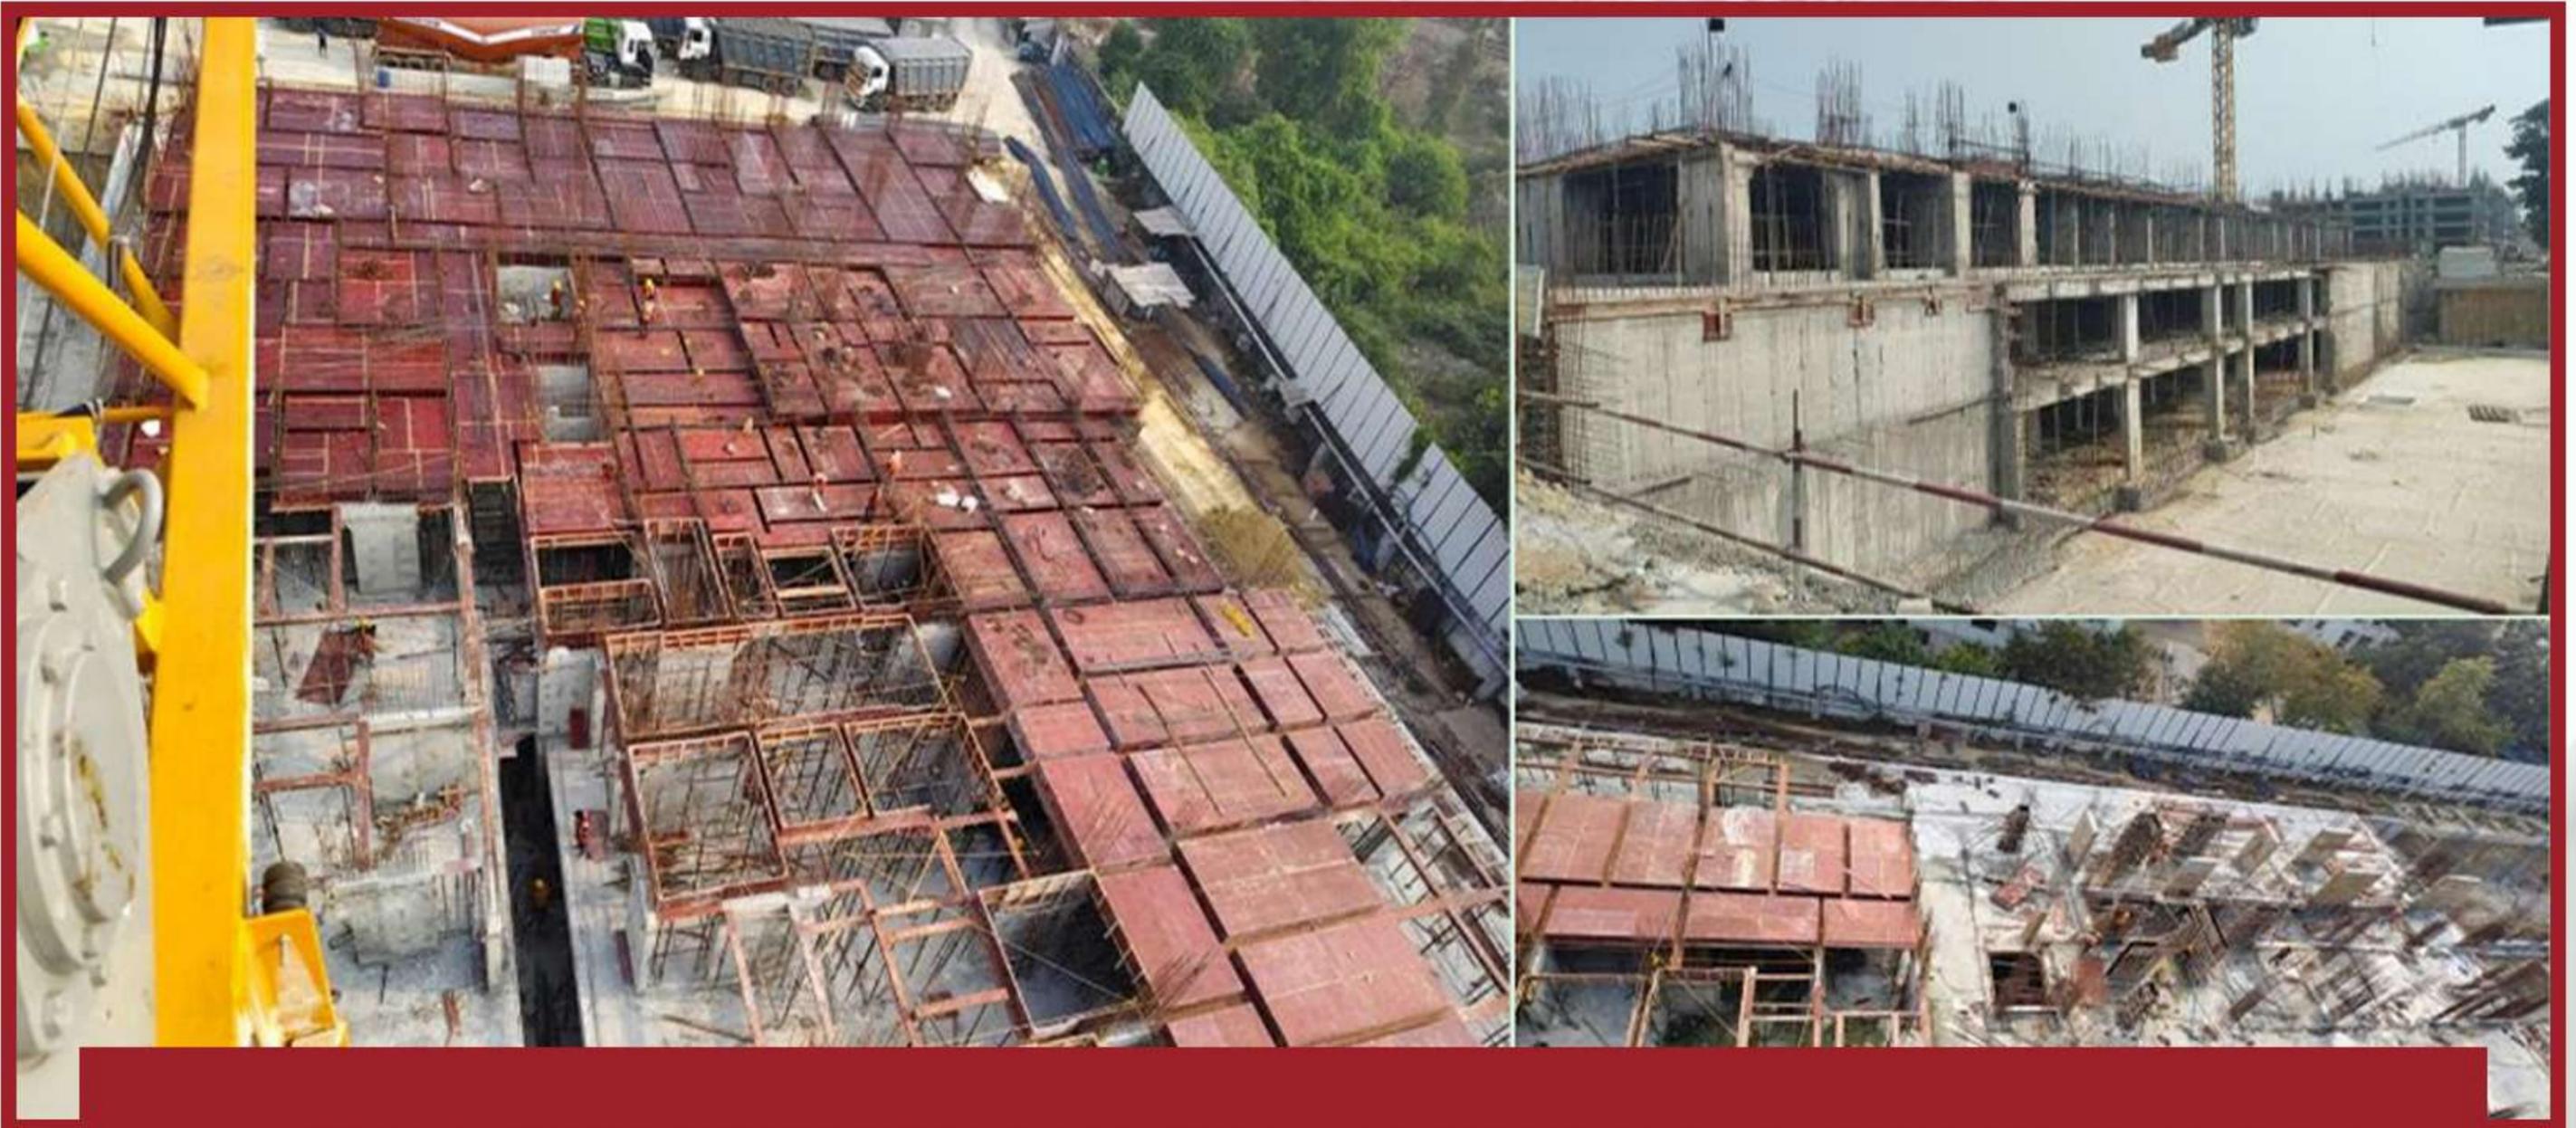

Block B - B1 ROOF SLAB LEVEL / upper basement slab concrete works has been completed

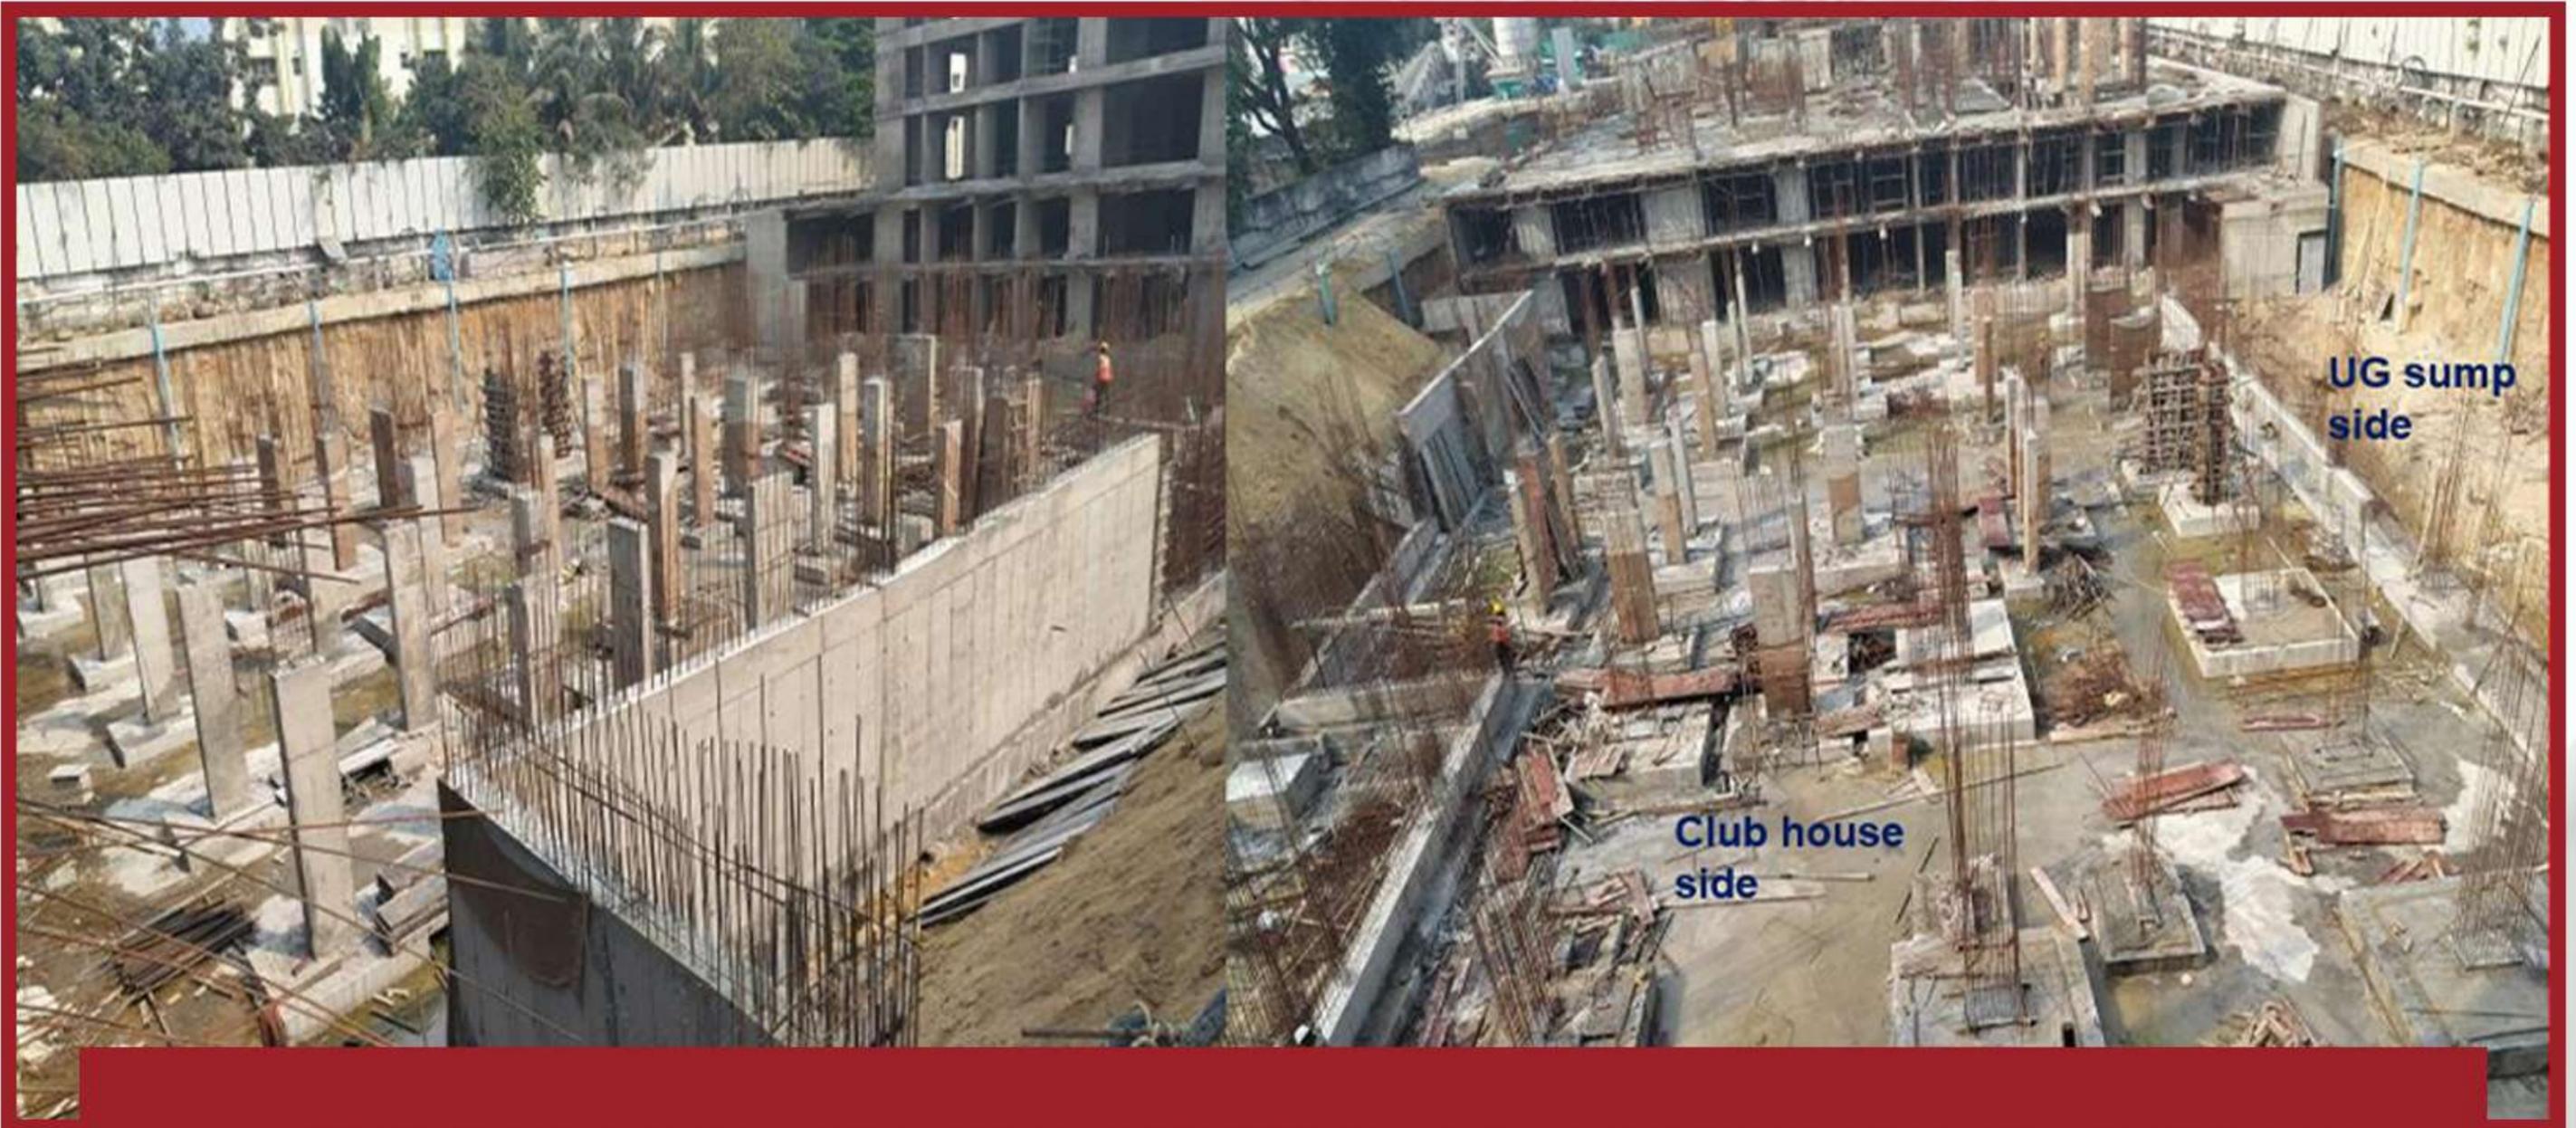

Block D / Club house –excavation , RAFT PCC & waterproofing works and raft-rcc works has

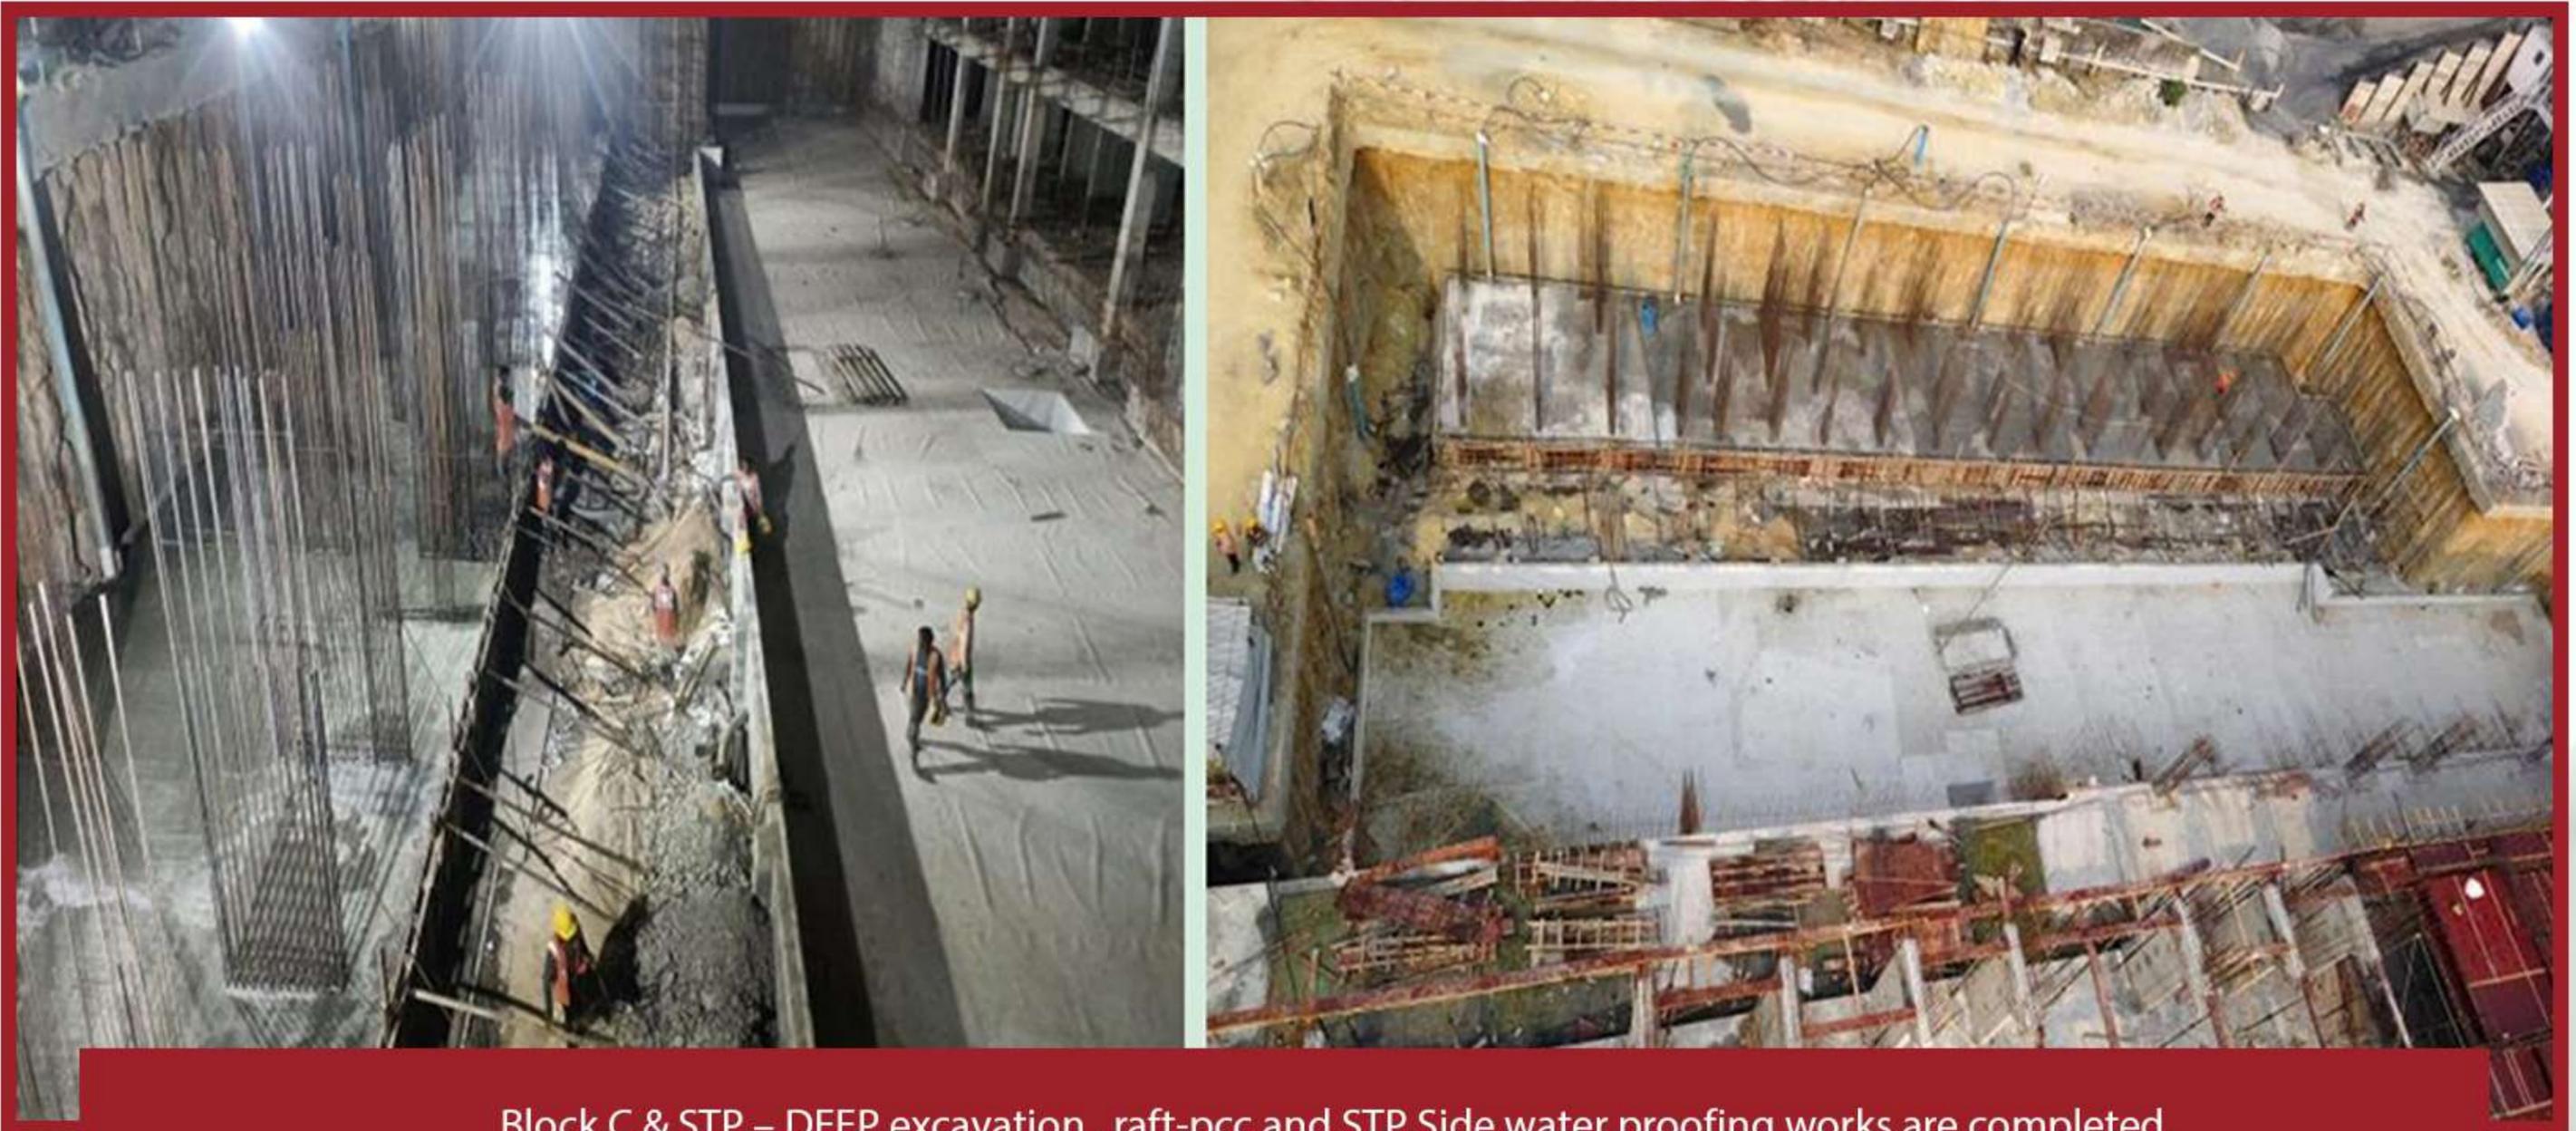

Block C & STP – DEEP excavation , raft-pcc and STP Side water proofing works are completed.
Block C – raft concrete completed on 27.2.26



Block -B West side retaining wall inner side upper basement area Tie rod hole packing

Club House West side water proofing preparation works

WATER PROOFING WORKS AND SOIL BACKFILLING WORKS
