

BLOCK - A




BLOCK - C



Block A – Tenth Floor Roof Slab Fully Completed. Eleventh Floor Roof Slab Works In Progress. block B – Fifth Floor Roof Slab Fully Completed. Sixth Floor Roof Slab Works In Progress. block C – First Floor Roof Slab Fully Completed. Second Floor Roof Slab Works In Progress. block D / Club House – Raft, B2 Level - Retaining Wall And Columns Concrete Completed, Roof Slab Rcc & Shuttering Works In Progress.



Block D / Club House –raft-rcc Works Has Been Completed b2 Level - Columns & Retaining Wall Concrete Works Are Completed. B2 Roof Level Slab Concrete South Side Completed & north Side Shuttering Works In Progress. External Waterproofing Works Completed.

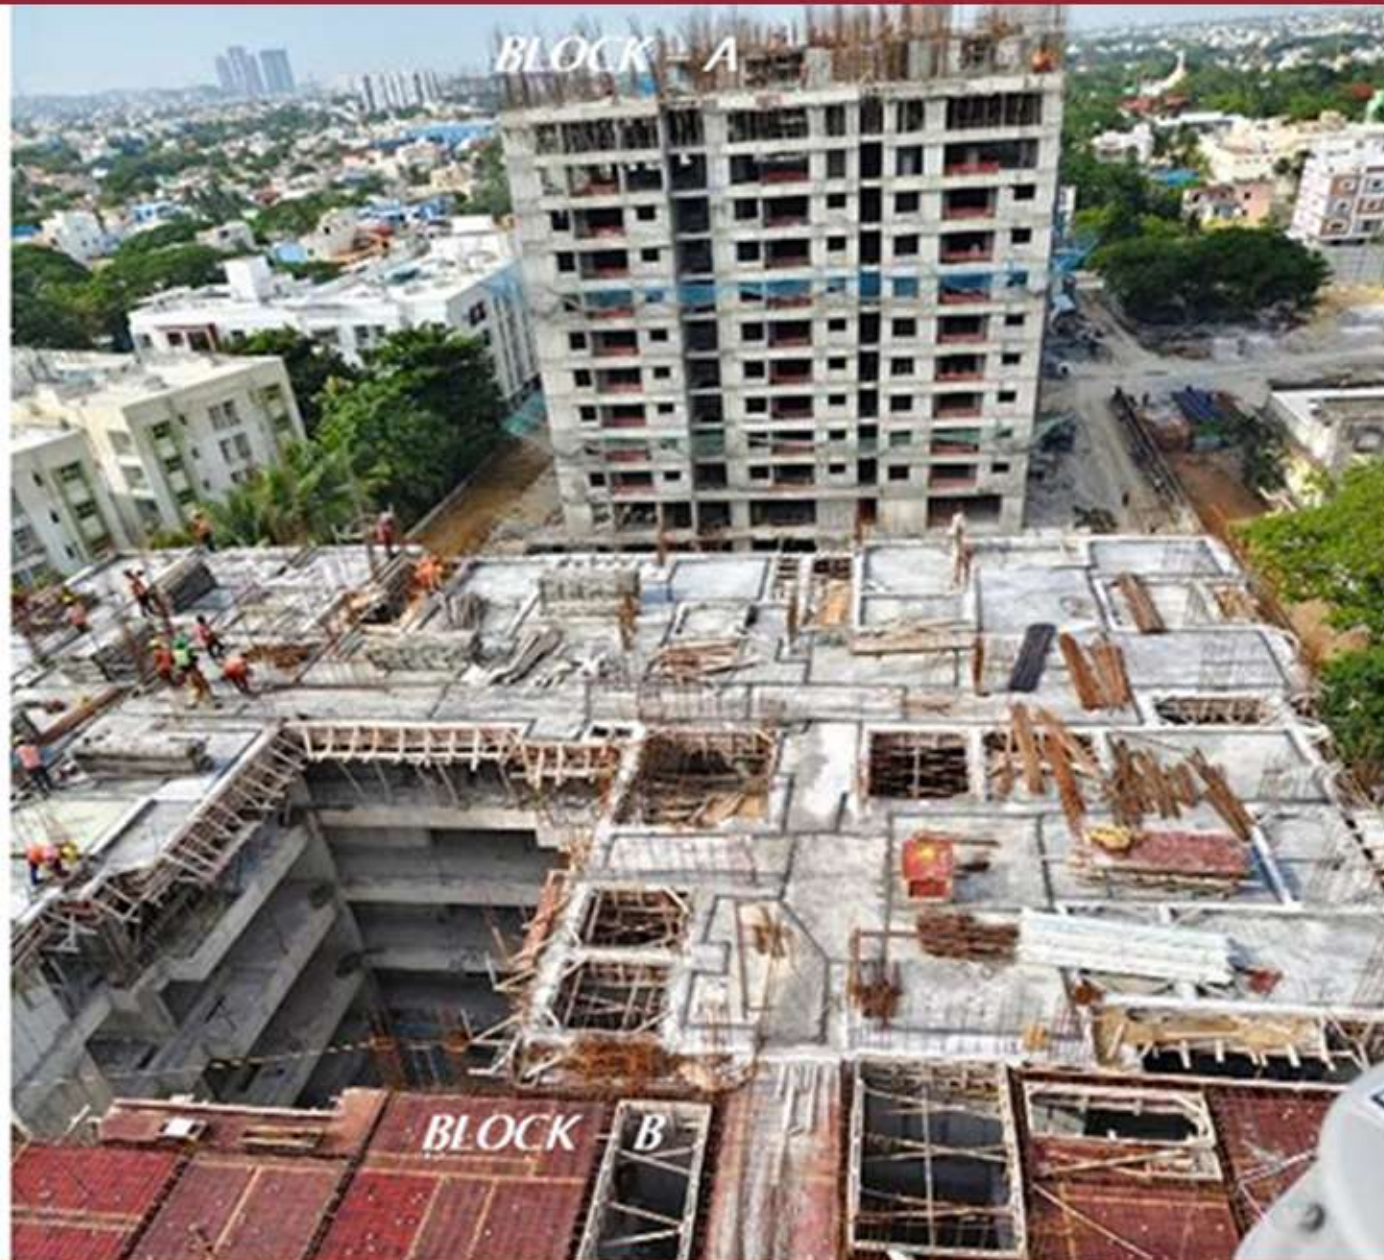

Block B, Club House & Block A

South Side



North Side



Block A :tenth Floor Roof Slab : Roof Slab Concrete Fully Completed On 25.7.26
eleventh Floor Roof Slab Pour 1 (Units 1- 5) Concrete Completed And Pour 2 (Unit-6,7,8,14,15&16) Slab Shuttering Works In Progress

WEST SIDE



Block A – Elevation

TOWARDS SOUTH -EAST SIDE FIRST FLOOR PODIUM LEVEL



*SOUTH SIDE
EXTERNAL SCAFFOLDING WORKS*



Block A – Elevation



Block A – Aac Block Works : Up To 8th Floor Lintel Level Aac B/w Completed . Wall Plastering - 1st & 2nd Floor Completed. 3rd & 4th Floor Work In Progress. Electrical Wall Chasing ,db Box & Conduit Instalation 1st -3rd Floor Completed. 4th Floor Wip.
phe First Fix : Toilet & Kitchen Plumbing Line Progress In 1 & 2 Nd Floor And Fire Fighting Line Works In Progress

NORTH SIDE



SOUTH SIDE



Block B : Fifth Floor – Roof Slab Concrete Fully Completed On 22.7.26
sixth Floor Pour 1 (Unit 1-5) Concrete Completed And Pour 2 (Unit 6-8 & 14-16) Slab Reinforcement Works In Progress.

NORTH WEST SIDE




Block B – Elevation

EAST SIDE



West side

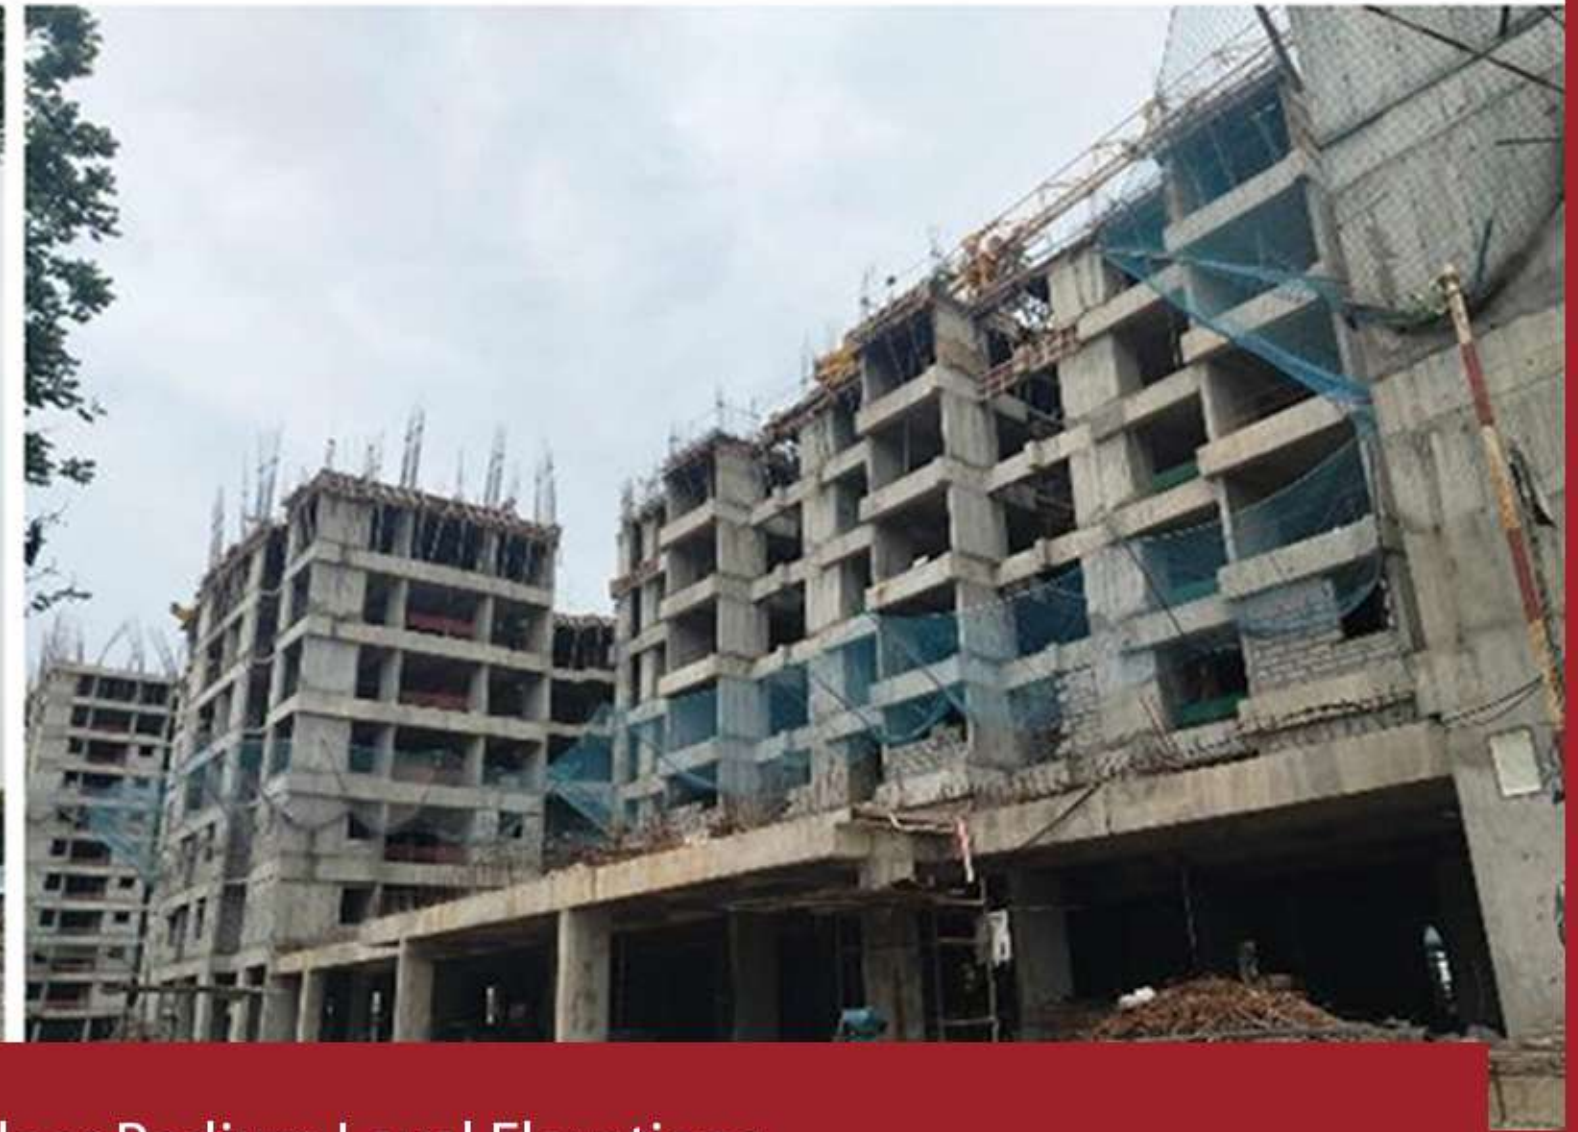

Block B –elevation / First Floor Podium Level Elevations

SOUTH SIDE



Block B – 1st & 2nd Floor Aac Block Works In Progress




Block C : First Floor Roof Slab / Second Floor Slab Concrete Works Completed On 30.7.26.
second Floor Roof Slab Level Column Works In Progress

COMPOUND WALL WORKS



Rainwater tank at clubhouse west side

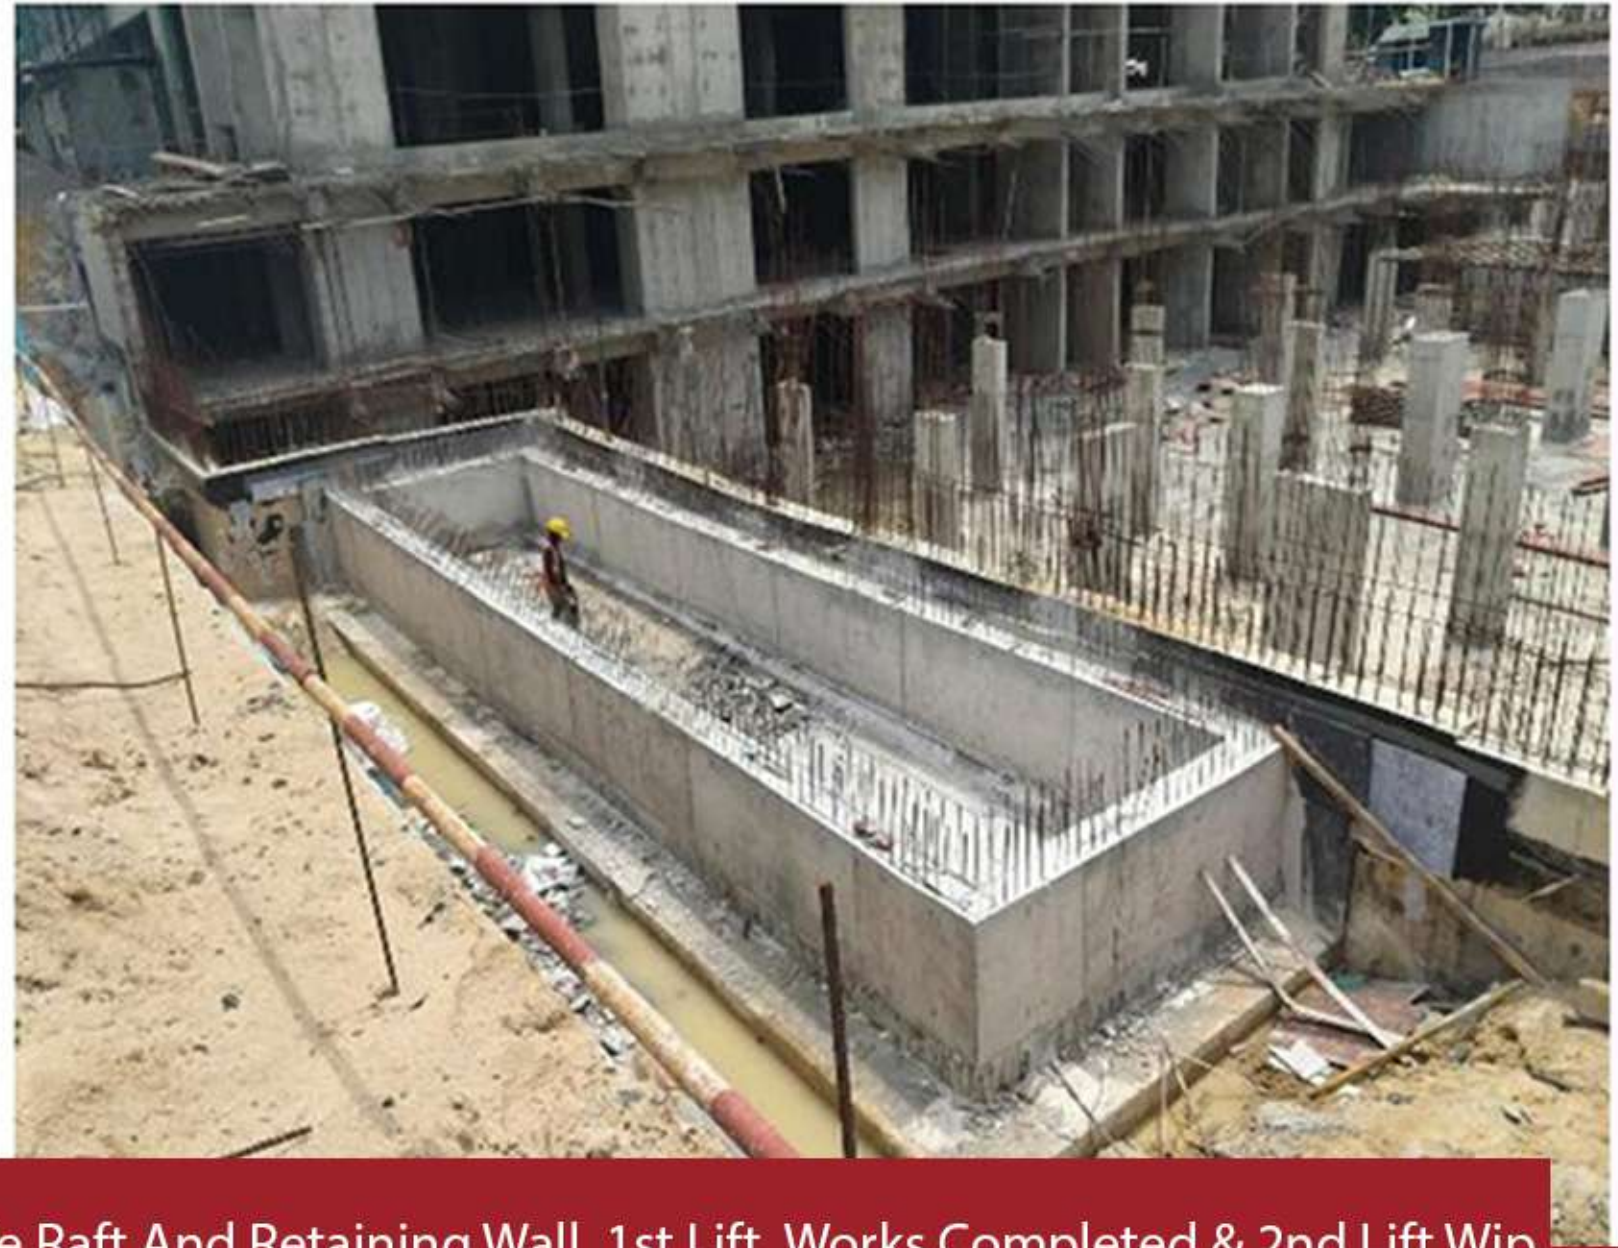

External Development : 1. Compound Wall Works: East Side Raft And Retaining Wall 1st Lift Works Completed & 2nd Lift Wip
2. Rainwater Tank At Clubhouse West Side : Raft Foundation And Wall Concrete Completed Till B2 Roof Slab Level
