



Block A –eighth Floor Roof Slab Completed. Ninth Floor Roof Slab Works In Progress. Block B – Third Floor Roof Slab Concrete Works Completed. Fourth Floor Roof Slab Works In Progress. Block C – Foundation Level Works Has Been Completed. Stilt Level Columns Completed & Roof Slab Works In Progress. Block D / Club House – Raft, B2 Level - Retaining Wall And Columns Concrete Completed, Roof Slab Shuttering Works In Progress.





Block D / Club House –raft-rcc Works Has Been Completed

b2 Level - Columns & Retaining Wall Concrete Works Are Completed.

raft Above Soil Filling & Pcc Completed. B2 Roof Level Slab Shuttering Works & External Wall Water Proofing Works In Progress





Block B, Club House & Block A



9<sup>th</sup> floor roof – North Side



10<sup>th</sup> floor roof – South Side




Block A : B2 Roof Slab On 10.10.25 , B1 Roof Slab On 15.11.25 And Stilt Roof Slab Completed On 14.12.25 1st Floor Roof Completed On 04.01.26 , 2nd Floor Roof Slab Completed On 25.01.26 , 3rd Floor Roof Slab Completed On 18.2.26, 4th Floor Roof Slab Completed On 17.3.26 & 5th Floor Roof Slab Completed On 4.4.26. Sixth Floor Roof Slab Completed On 02.05.26 Seventh Floor Roof Slab Completed On 27.5.26. Eighth Floor Roof Slab Completed On 16.6.26. Ninth Floor Roof Slab : Pour 1 ( Units 1- 5 ) Concrete Completed, Pour 2 – Slab Reinforcement And Pour 3 – Slab Shuttering Works In Progress. Tenth Floor Roof Slab – Pour 1 Columns Wip.






BLOCK A – ELEVATION



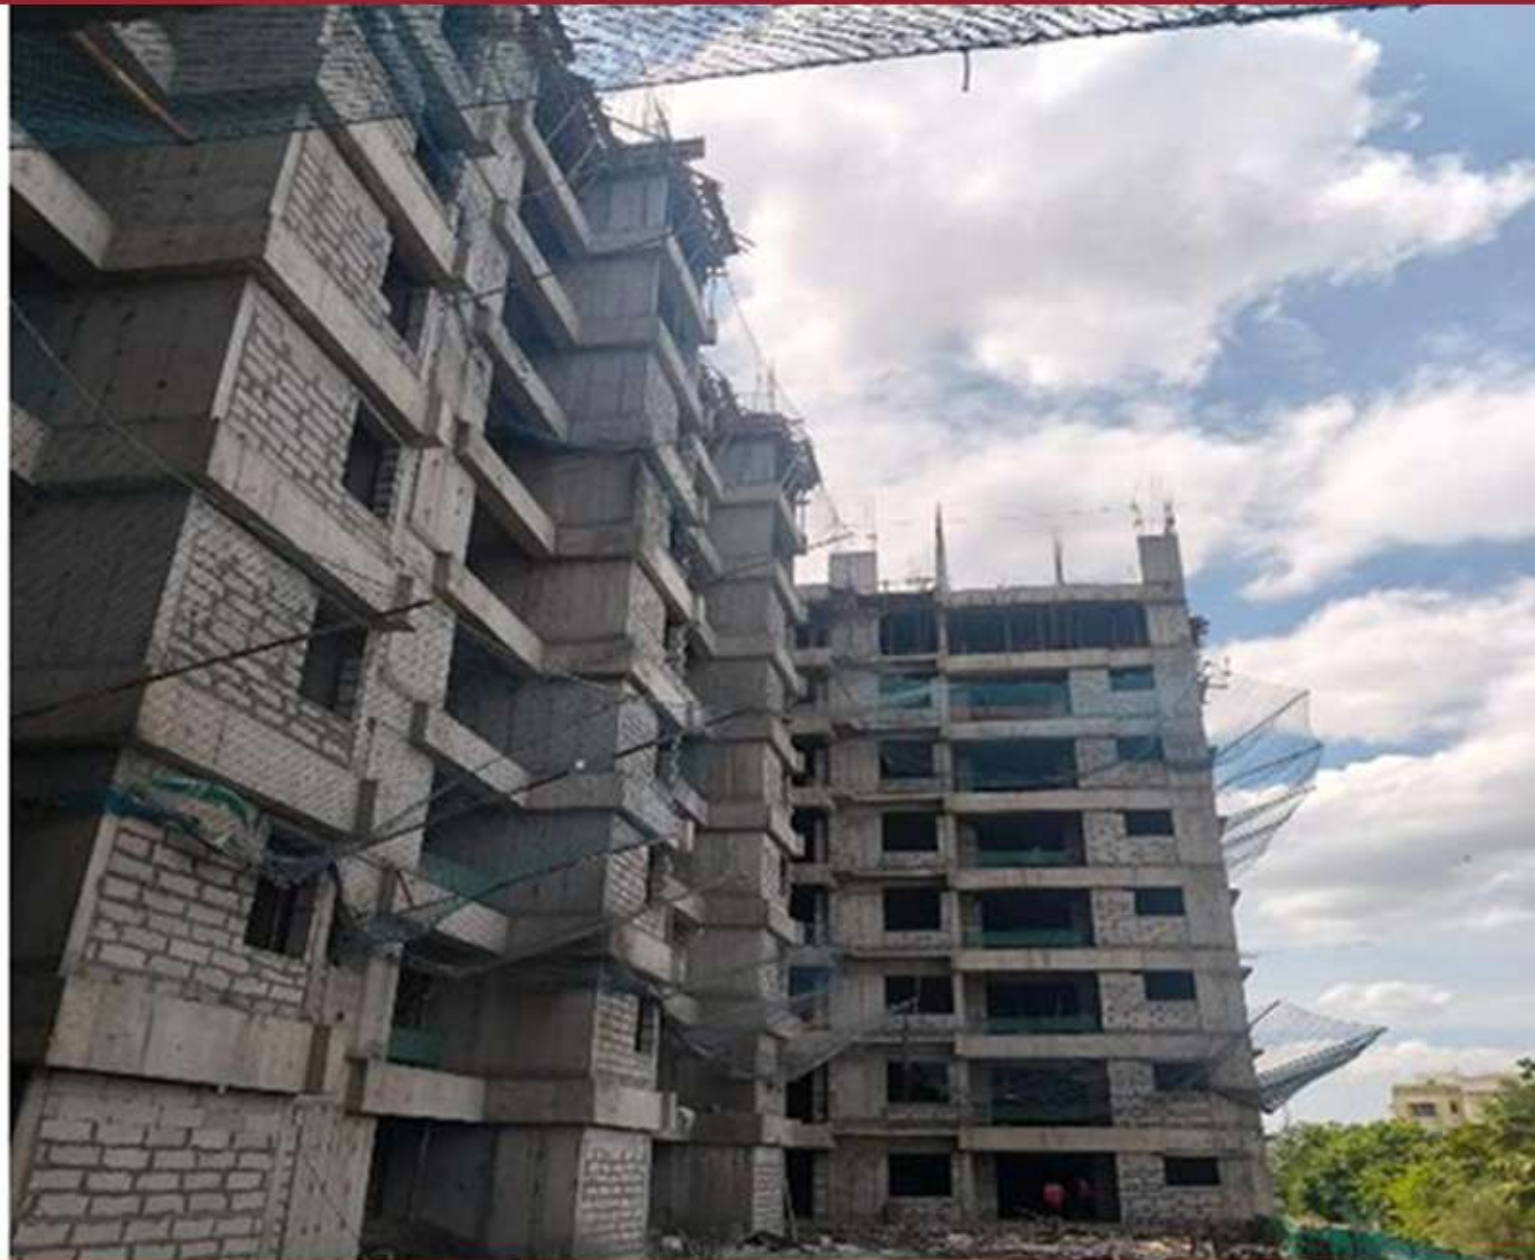

Block A –first Floor Podium Leve; Elevation



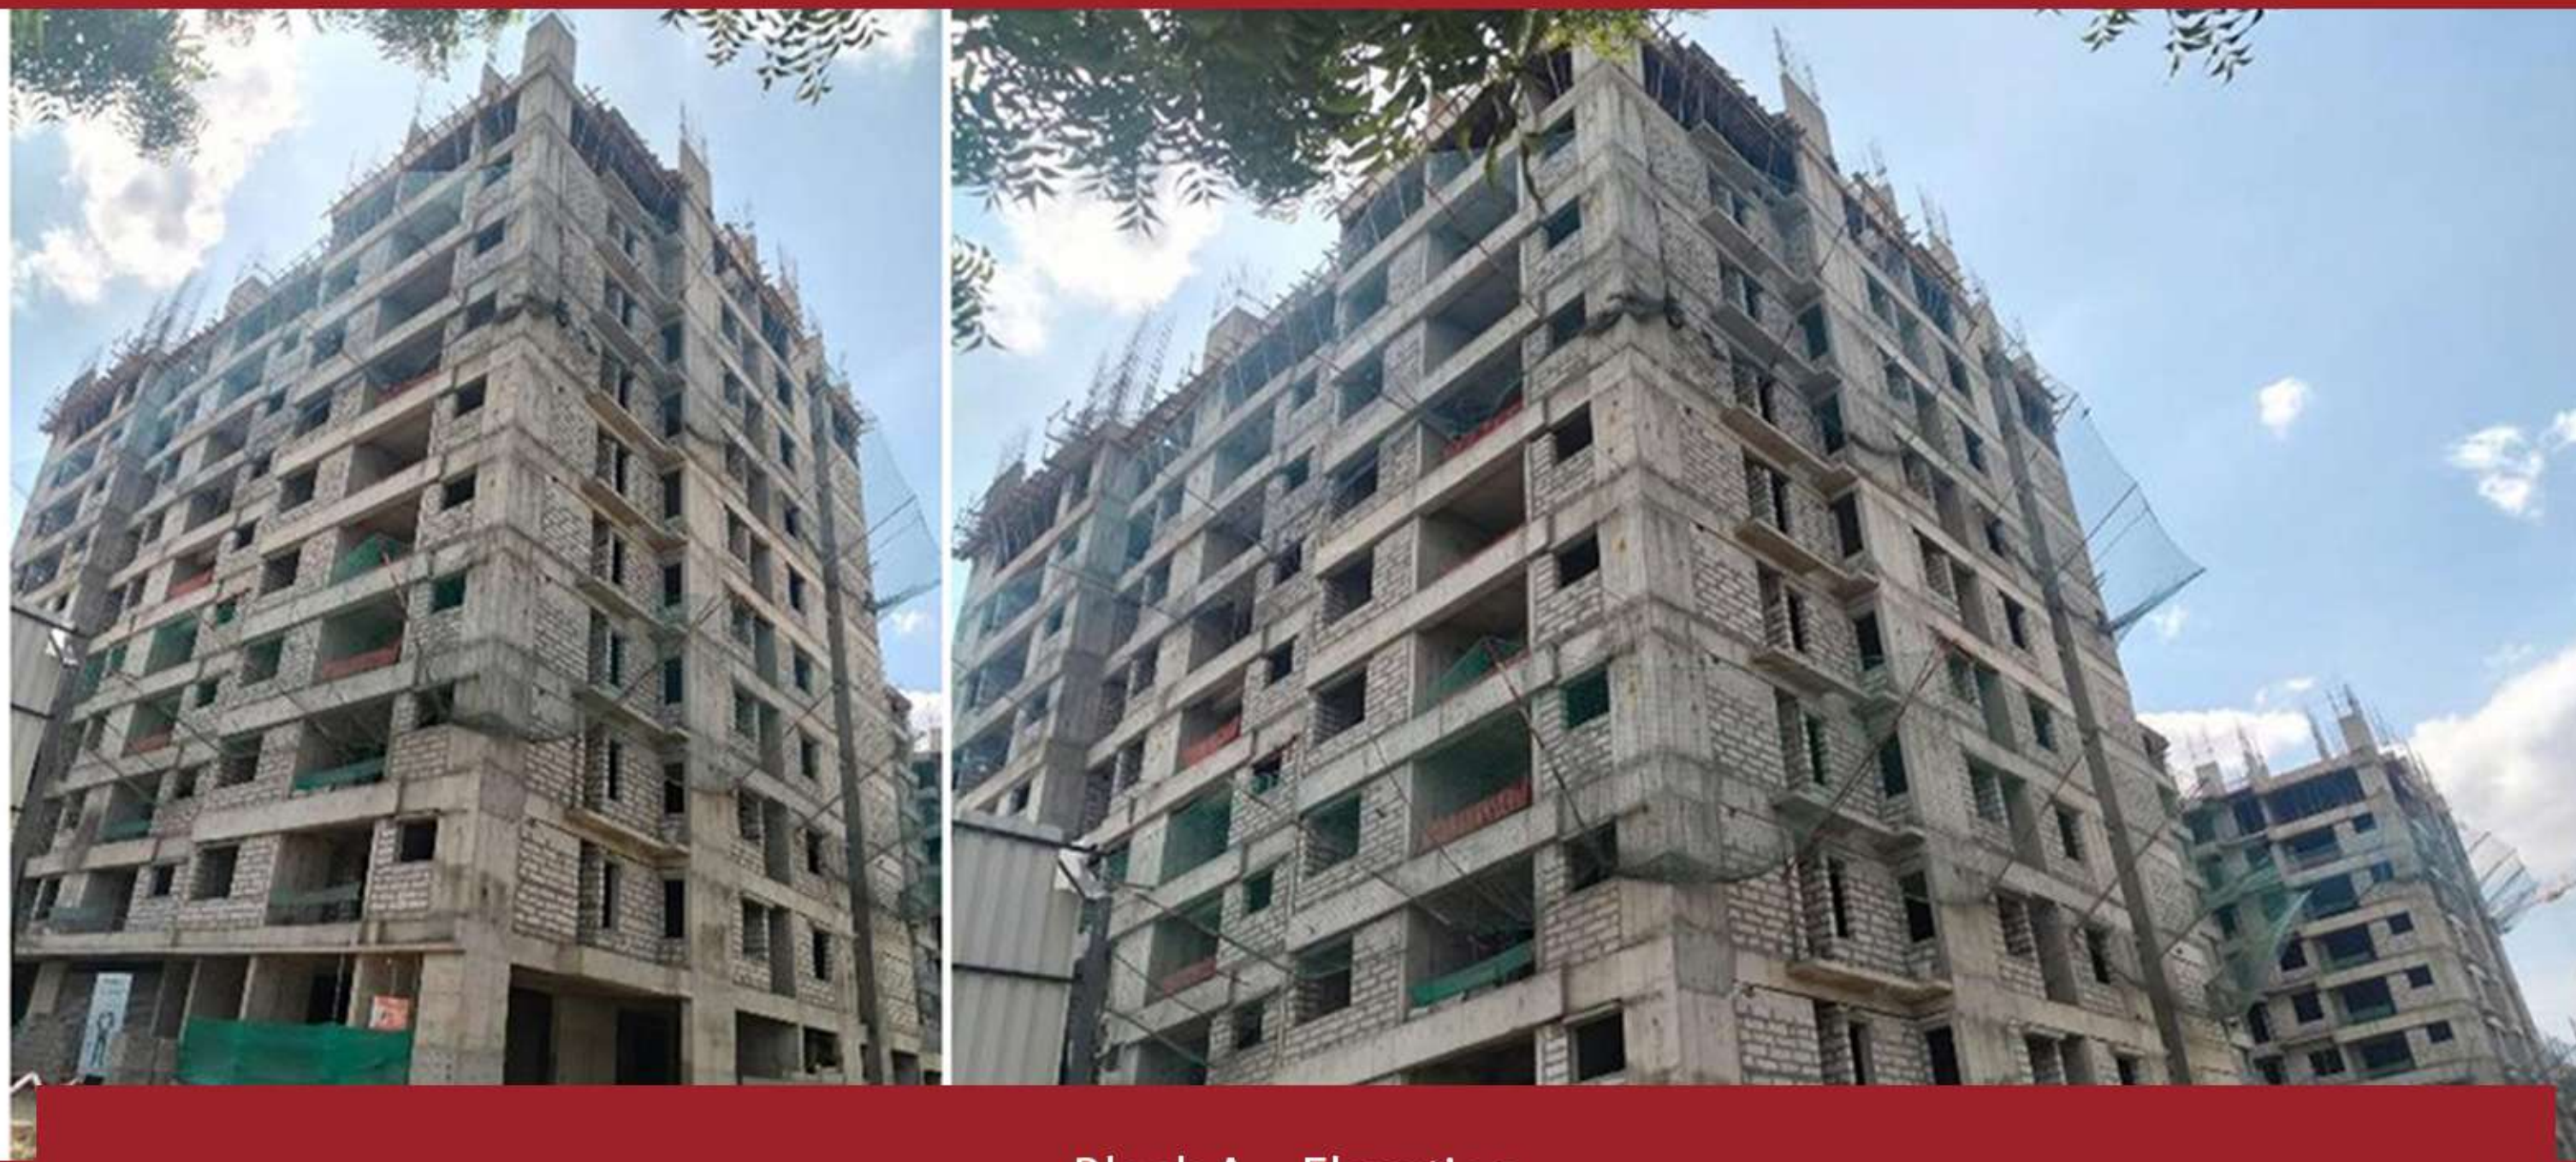

Block A – Elevation



NORTH SIDE



SOUTH SIDE




Block B : Stilt Floor Roof / First Floor Slab Concrete Completed On 01.04.26 And 1st Floor Roof Level – / Second Floor Slab Concrete Completed On 10.05.26. 2nd Floor Roof Level / Third Floor Slab Concrete Completed On 30.5.26. third Floor Roof Slab Concrete Completed On 20.6.26. fourth Floor – Pour 1 Slab Concrete Completed. Pour 2 ( Unit 6-8 & 14-16 ) Slab Reinforcement And Pour 3 Slab Shuttering Wip. Fifth Floor – Pour 3 Columns Works In Progress.





Block B– Elevation



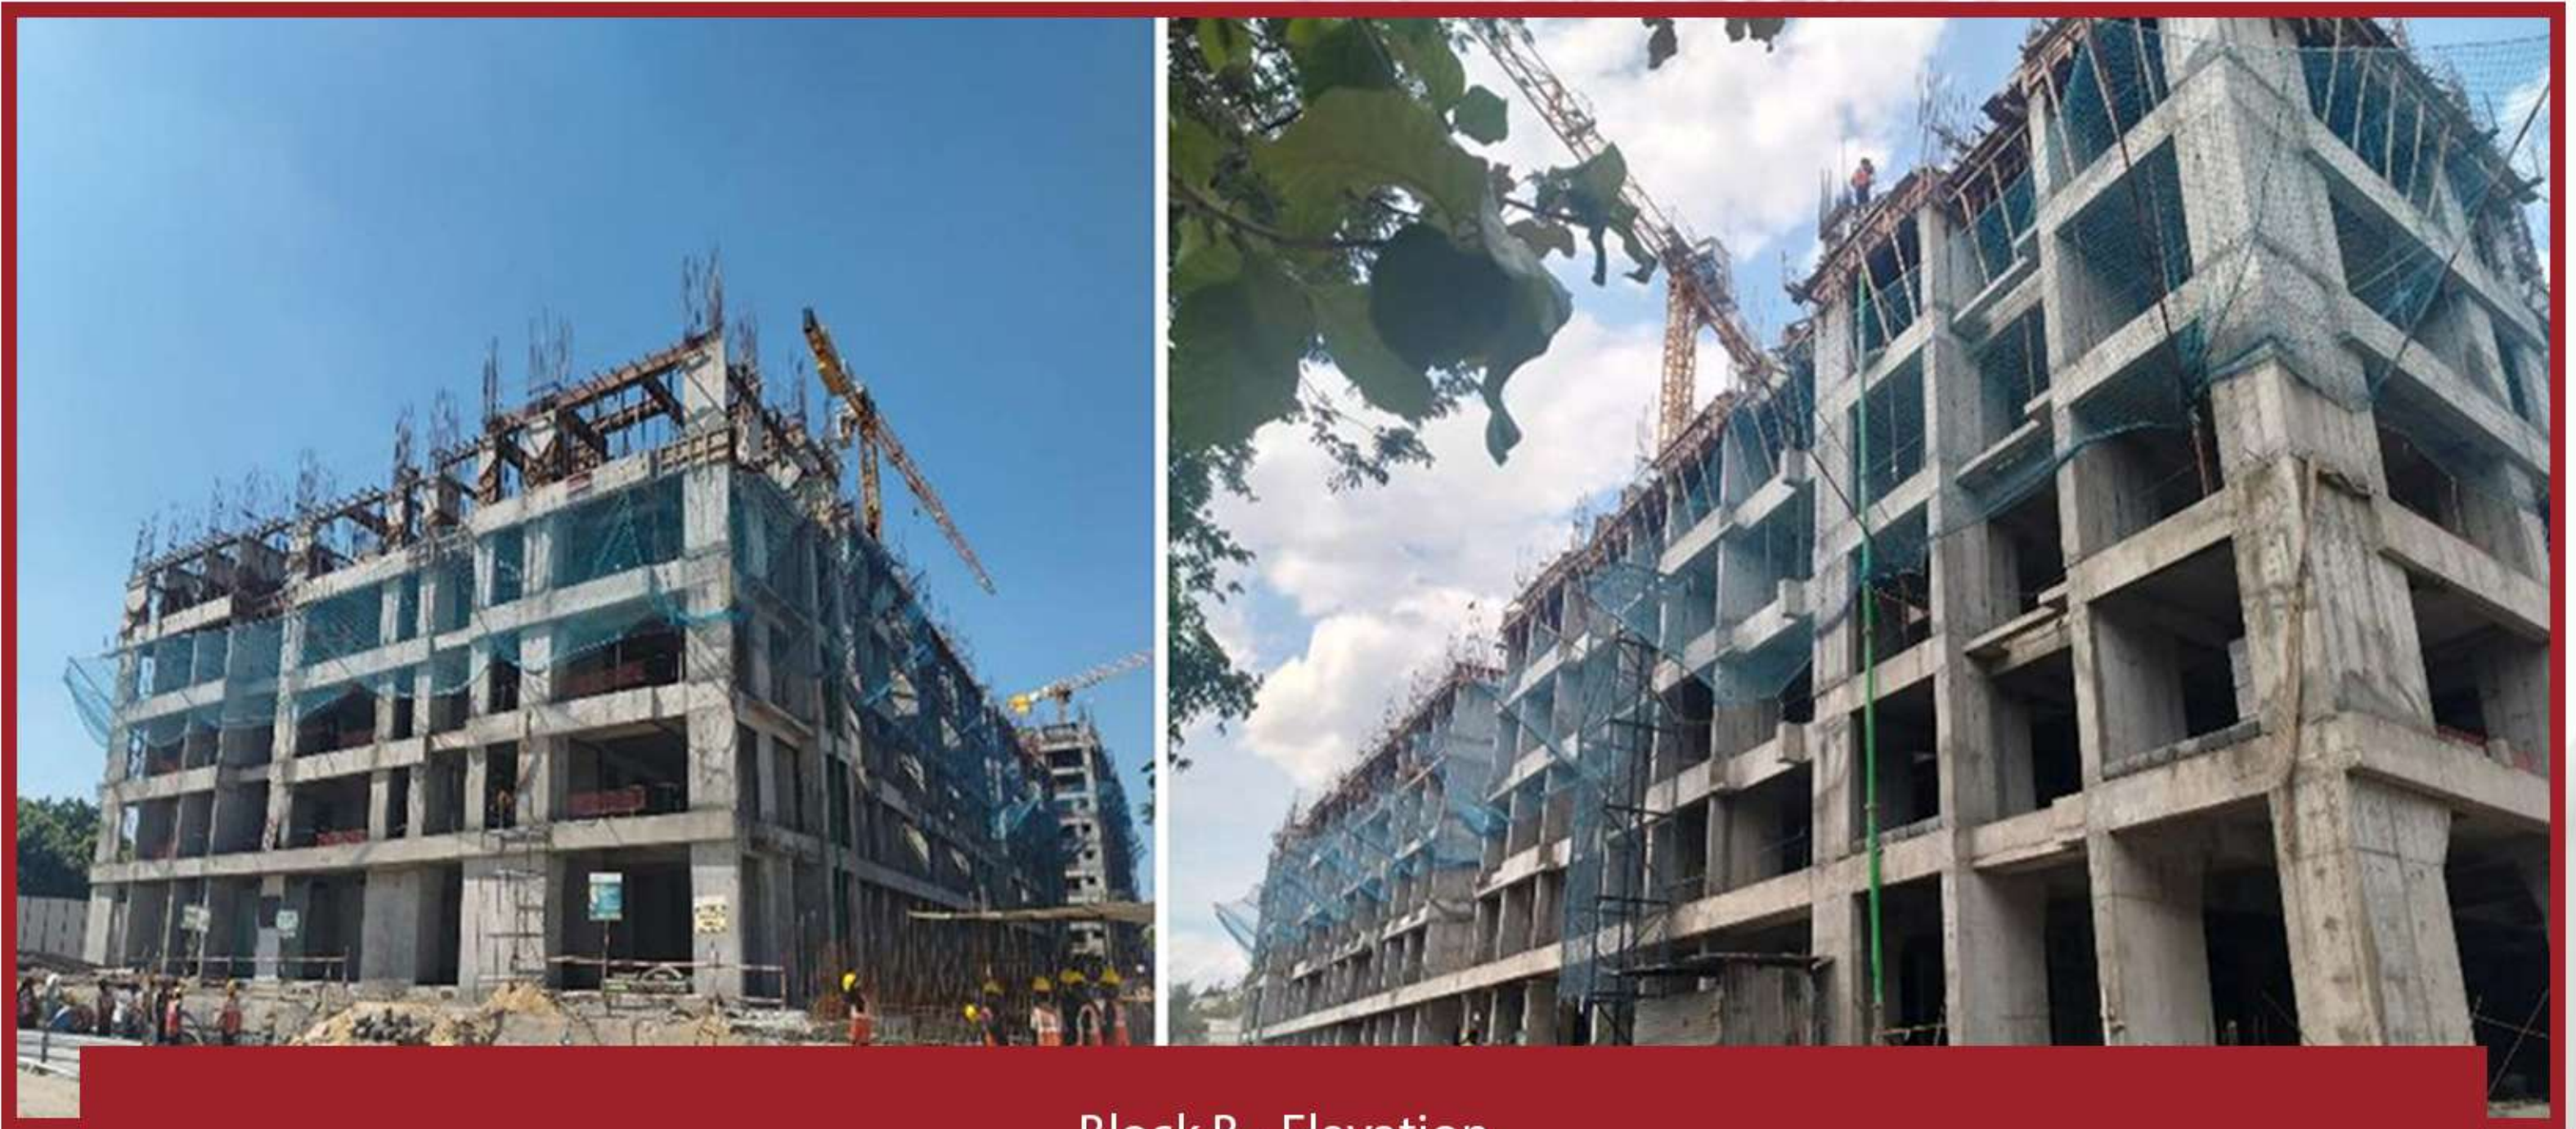

Block B– Elevation





Block C : Raft Concrete Completed On 27.2.26 , B1 & B2 Columns Works CompletD On 18.4.26.soil Filling & Plinth Beam Rcc Completed. Stilt Level Columns Works Completed On 21.6.26 And Slab Shuttering & Reinforcement Works In Progress. stp – Raft Completed On 18.3.26. Outer Retaining Wall Works Completed. Inner Wall In Progress






Block C -Elevations





Block A – Aac Block Works Up To 4th Floor Completed And 5th To 8th Floor Works & Lintel Works In Progress 1st & 2nd Floor Electrical Wall Chasing ,db Box & Conduit Instalation And Wall Plastering Work In Progress



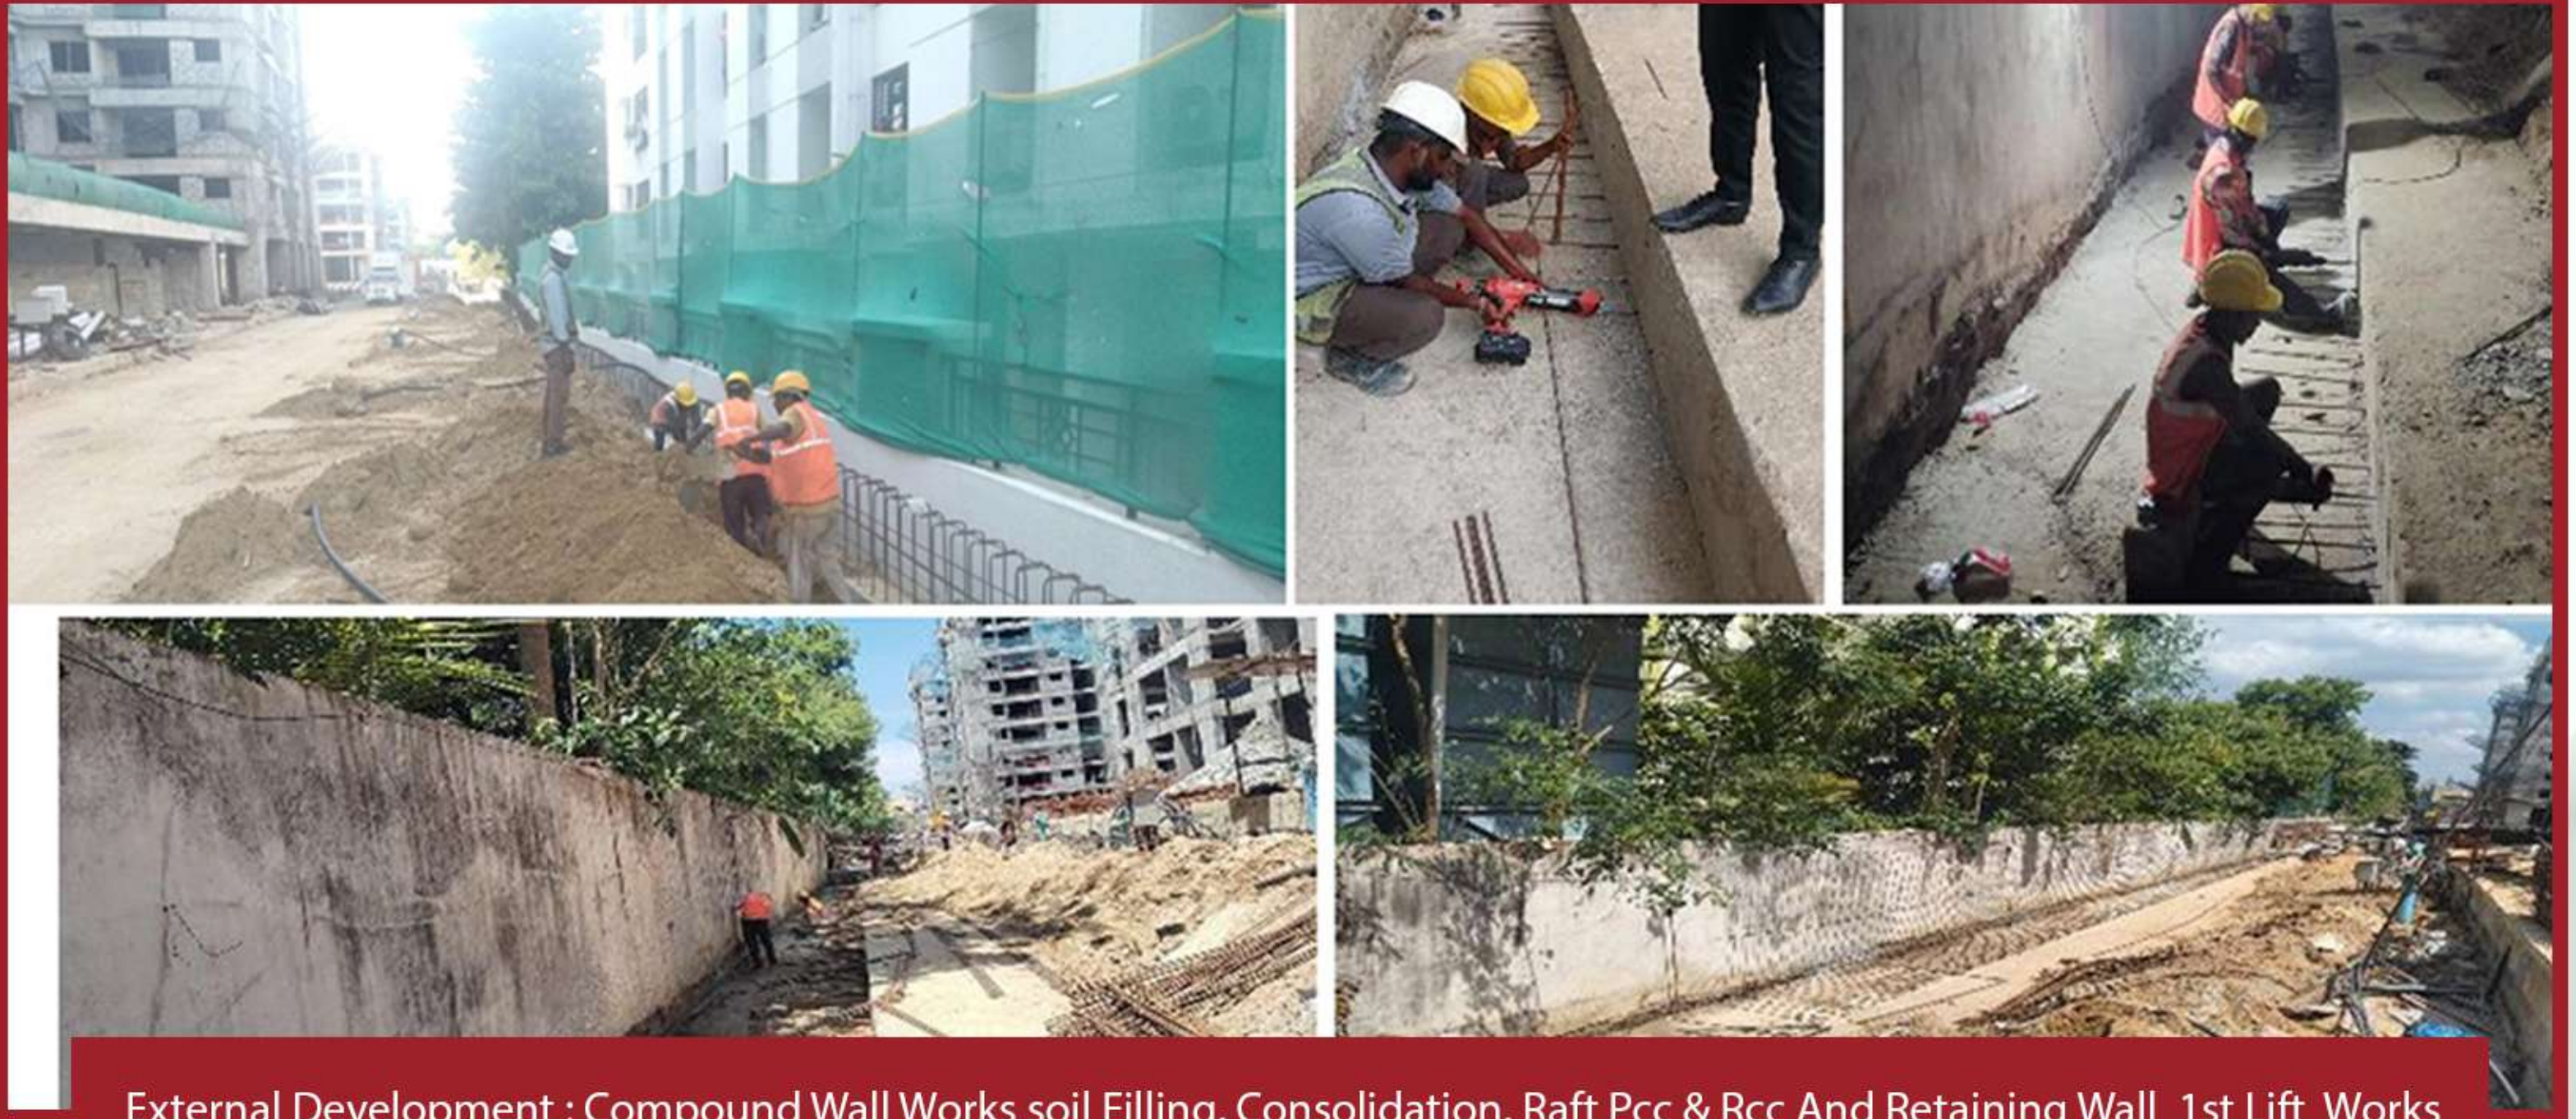

External Development : Compound Wall Works soil Filling, Consolidation, Raft Pcc & Rcc And Retaining Wall 1st Lift Works Completed Till Block B. earth Work & Raft Pcc / Rcc Works With Hilti Instalation Progress In Block B – West Side





Site Model Flat –block A Unit 103 : Block Works , Toilets & Kitchen Plastering Works Has Been Completed  
electrical Conduit And Metal Box Fixing Completed. Living & Bedroom Wall Plastering Progress In Living And Bedrooms
