


Block B, Club House & Block A

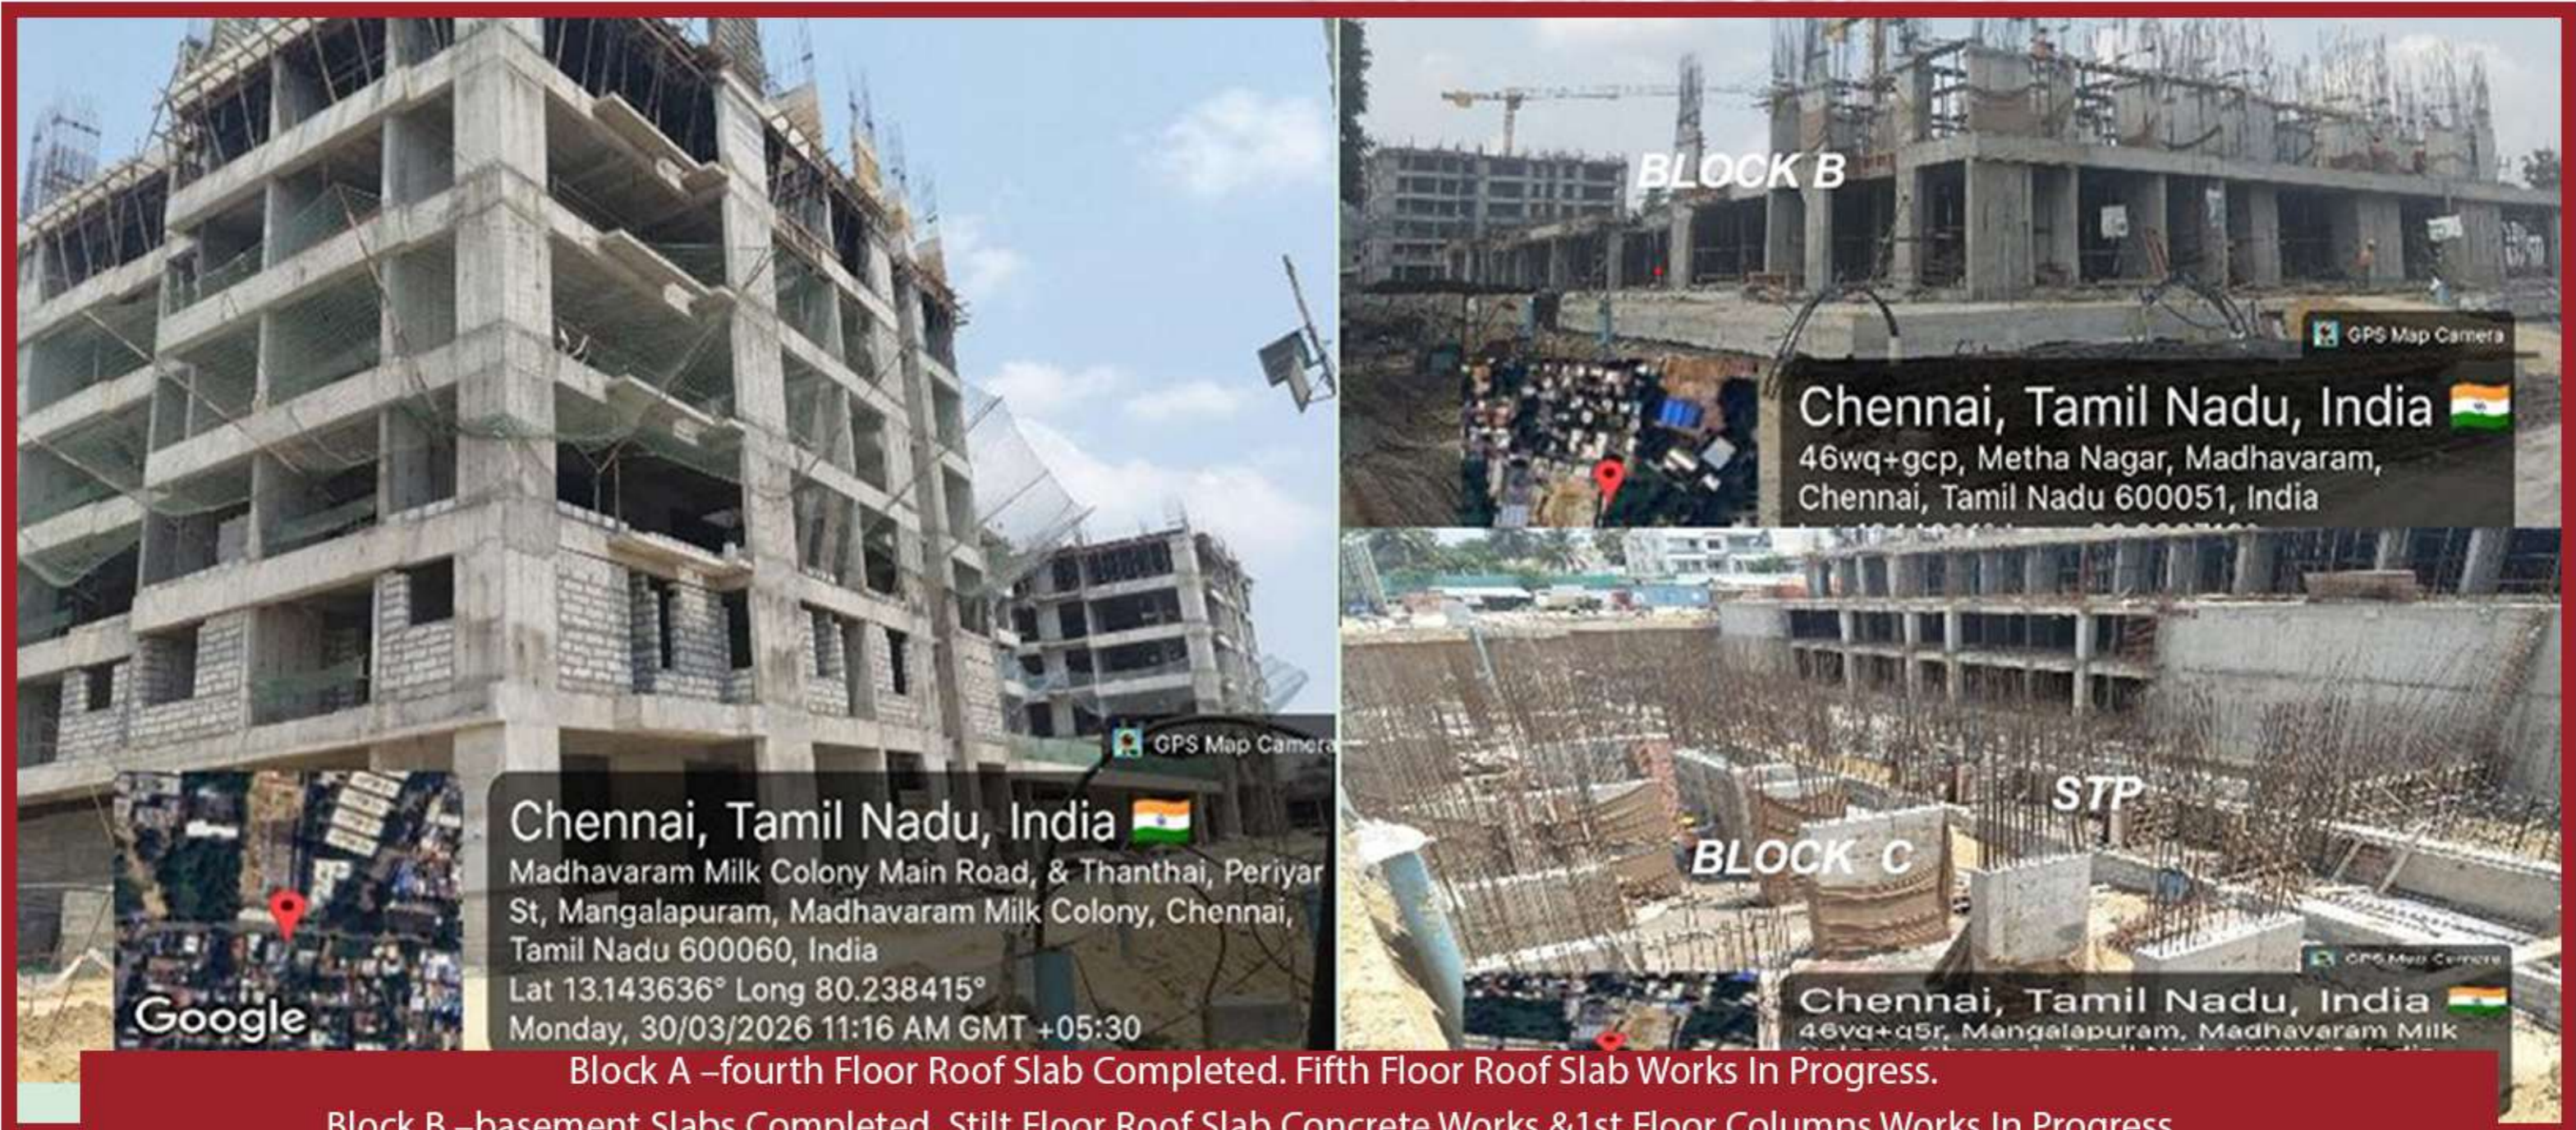

Chennai, Tamil Nadu, India 🇮🇳
Madhavaram Milk Colony Main Road, & Thanthai, Periyar
St, Mangalapuram, Madhavaram Milk Colony, Chennai,
Tamil Nadu 600060, India
Lat 13.143636° Long 80.238415°
Monday, 30/03/2026 11:16 AM GMT +05:30

Chennai, Tamil Nadu, India 🇮🇳
46wq+gcp, Metha Nagar, Madhavaram,
Chennai, Tamil Nadu 600051, India

Chennai, Tamil Nadu, India 🇮🇳
46vq+q5r, Mangalapuram, Madhavaram Milk

Block A –fourth Floor Roof Slab Completed. Fifth Floor Roof Slab Works In Progress.

Block B –basement Slabs Completed. Stilt Floor Roof Slab Concrete Works &1st Floor Columns Works In Progress.

Block D / Club House – Raft Concrete Completed . B2 Level - Retaining Wall And Columns Works In Progress.

Block C - Raft Concrete Works Has Been Completed. Columns & Retaining Wall Works In Progress



BLOCK A – External views



Block A – B2 Roof Slab On 10.10.25 , B1 Roof Slab On 15.11.25 And Stilt Roof Slab Completed On 14.12.25 first Floor Roof Completed On 04.01.26 And Aac Block Works Wip second Floor Roof Slab Completed On 25.01.26 And Third Floor Roof Slab Completed On 18.2.26 fourth Floor Roof Slab Completed On 17.3.26 fifth Floor Roof Slab Level – South & Central Side / Pour 1 & 2 Concrete Completed (Units 1-5 And Units 06,07,08,14,15 &



BLOCK A – AAC BLOCK WALL WORKS IN THE FIRST & second FLOOR LEVEL




Block B - B1 Roof Slab Level / Upper Basement Slab Concrete Works Has Been Completed On 21.2.26
first Floor Slab Level : North & Central Side - Slab Concrete Completed And South Side Works In Progress.
first Floor Roof Level - Column & Slab Bottom Works In Progress



**BLOCK D / CLUB HOUSE –RAFT-RCC WORKS HAS BEEN COMPLETED
B2 LEVEL - RETAINING WALL AND COLUMNS CONCRETE WORKS IN PROGRESS**



**BLOCK C – RAFT CONCRETE COMPLETED ON 27.2.26 AND STP – RAFT COMPLETED ON 18.3.26
STP RETAINING WALL AND BLOCKC – COLUMNS WORKS ARE IN PROGRESS**

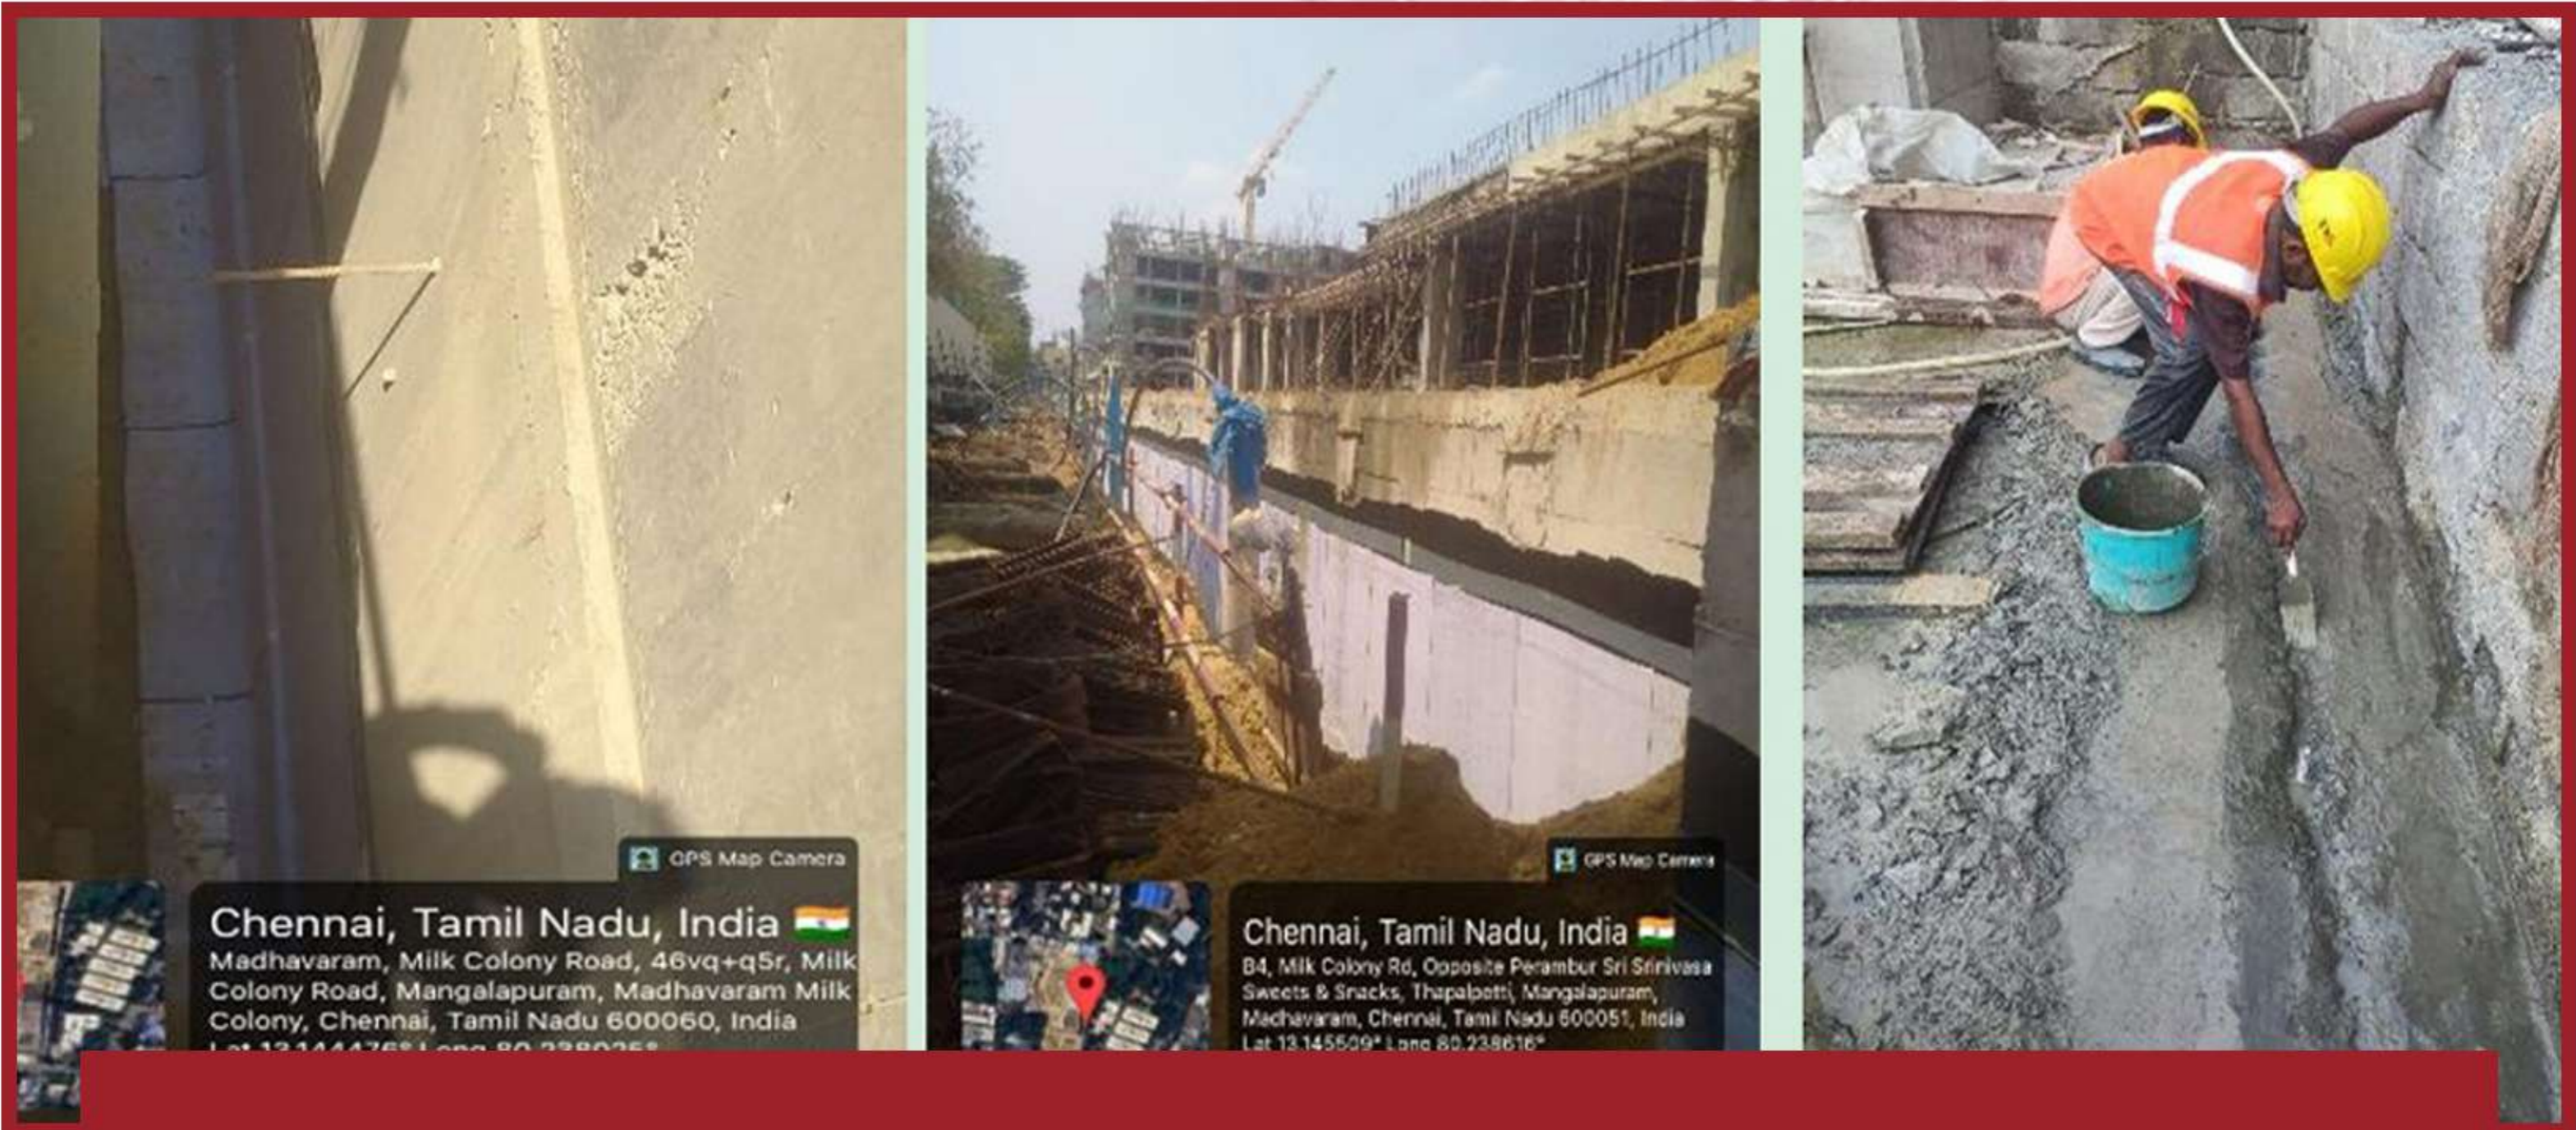

Water Proofing And Soil Backfilling Works
