





Block A – Raft And All Column Concrete , Retaining Wall Completed In South & West Side And North East Side Wip
B2 Roof Slab Pour 1 & Ramp 1 Concrete Completed In South West Side 259 Cum.
Shuttering And Reinforcement Works Progress In East Side



Block A - East Side / Pour 2 Slab Shuttering And Reinforcement Works Progress In Ramp 1 East Side

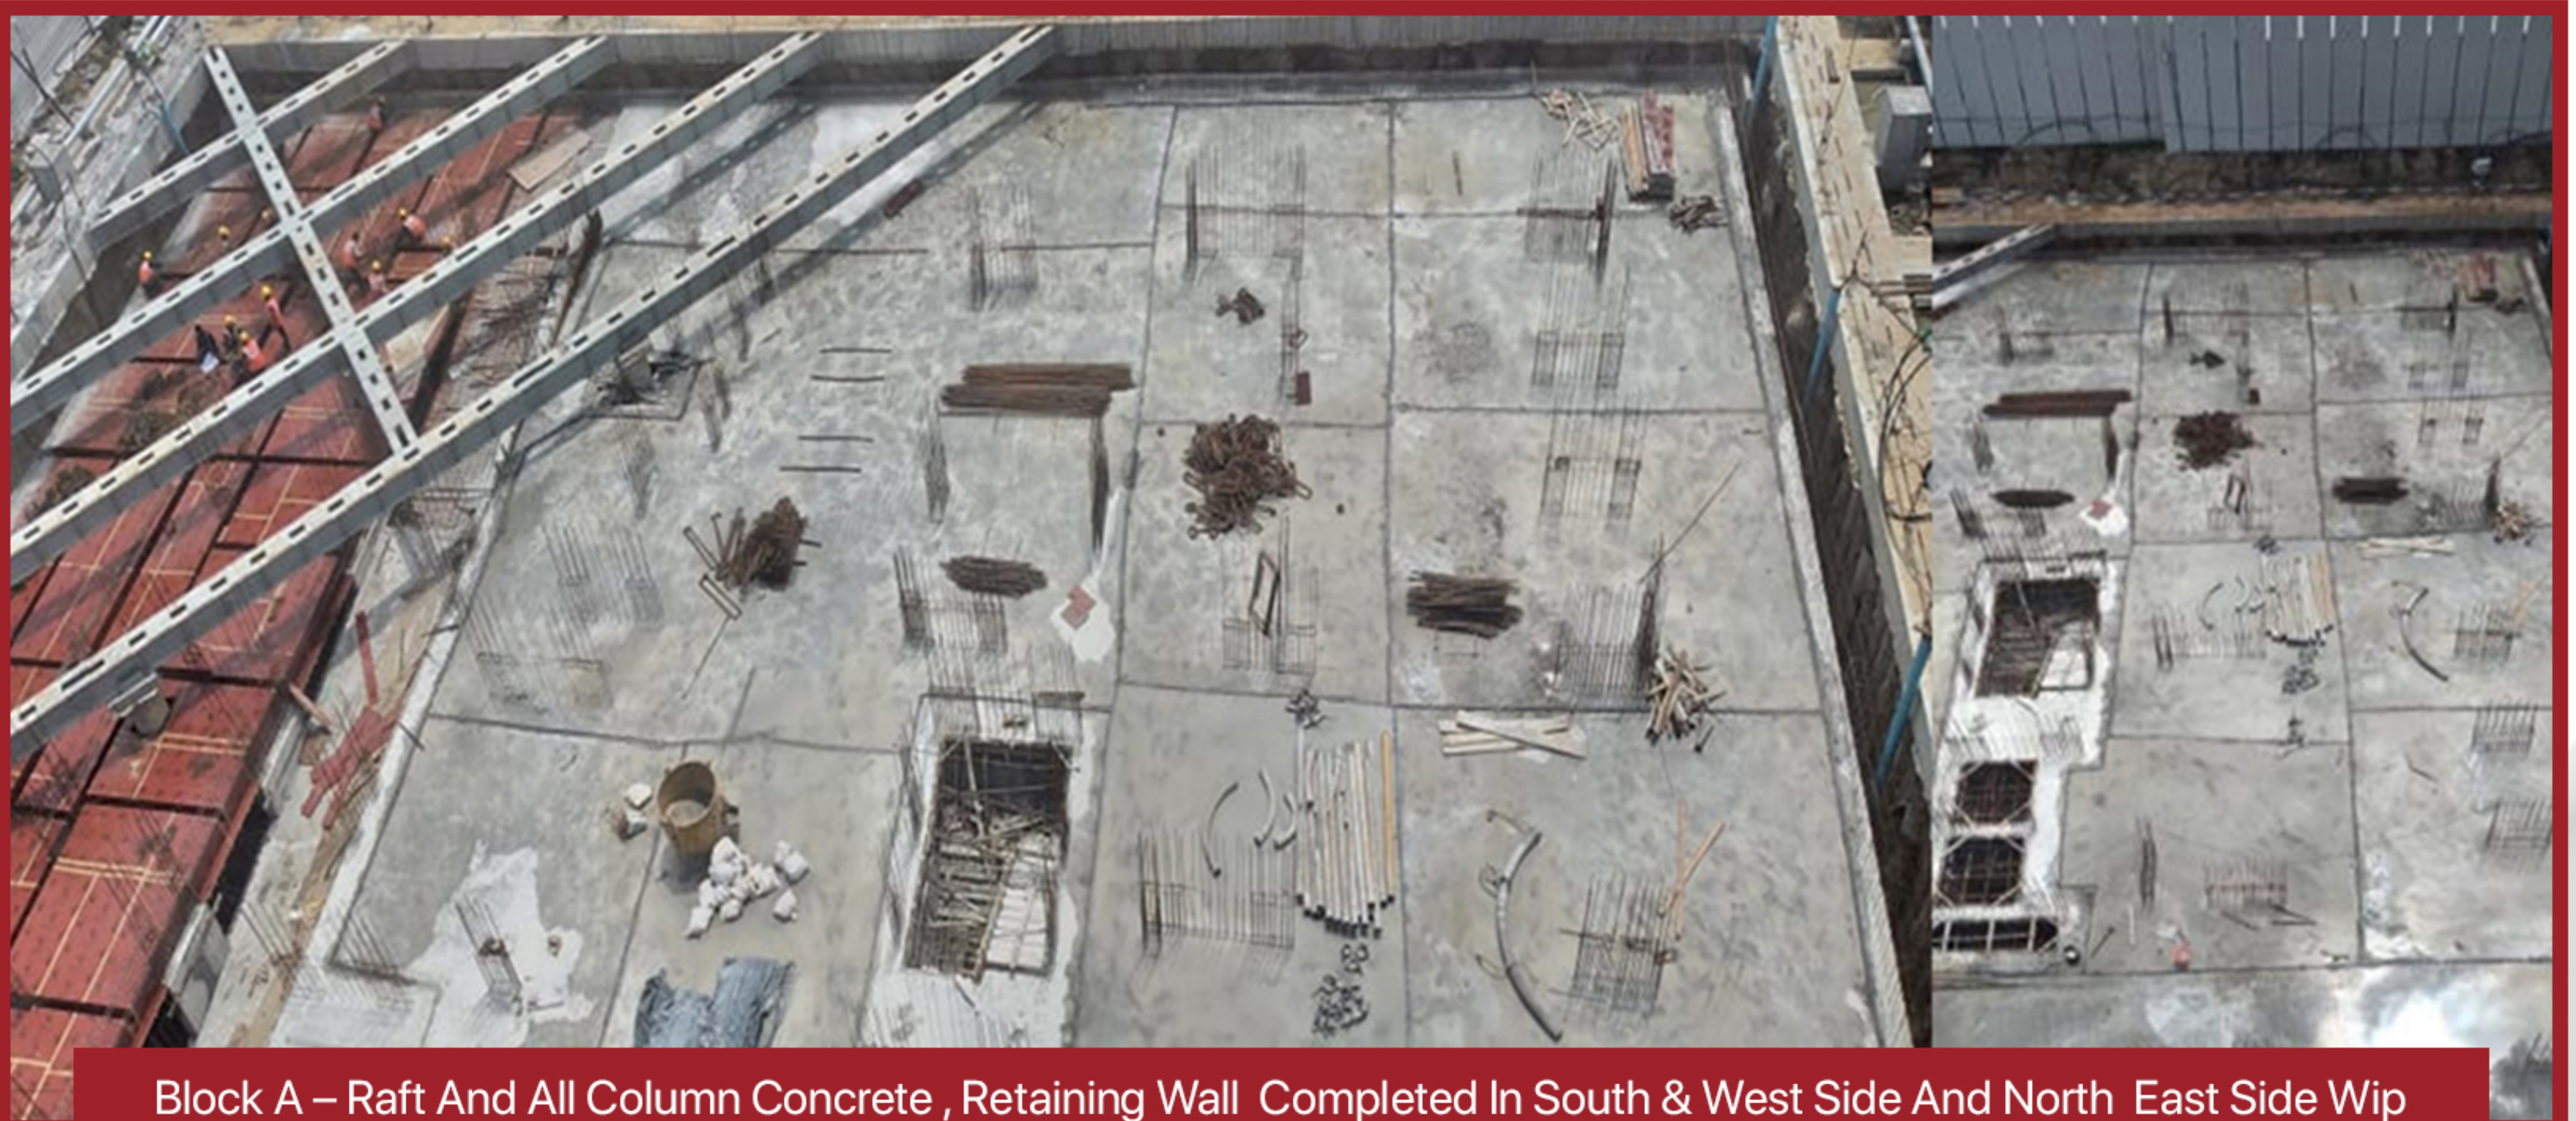


Block A Soil Filling Above Raft And Levelling Pcc Completed And West Side Retaining Wall Completed

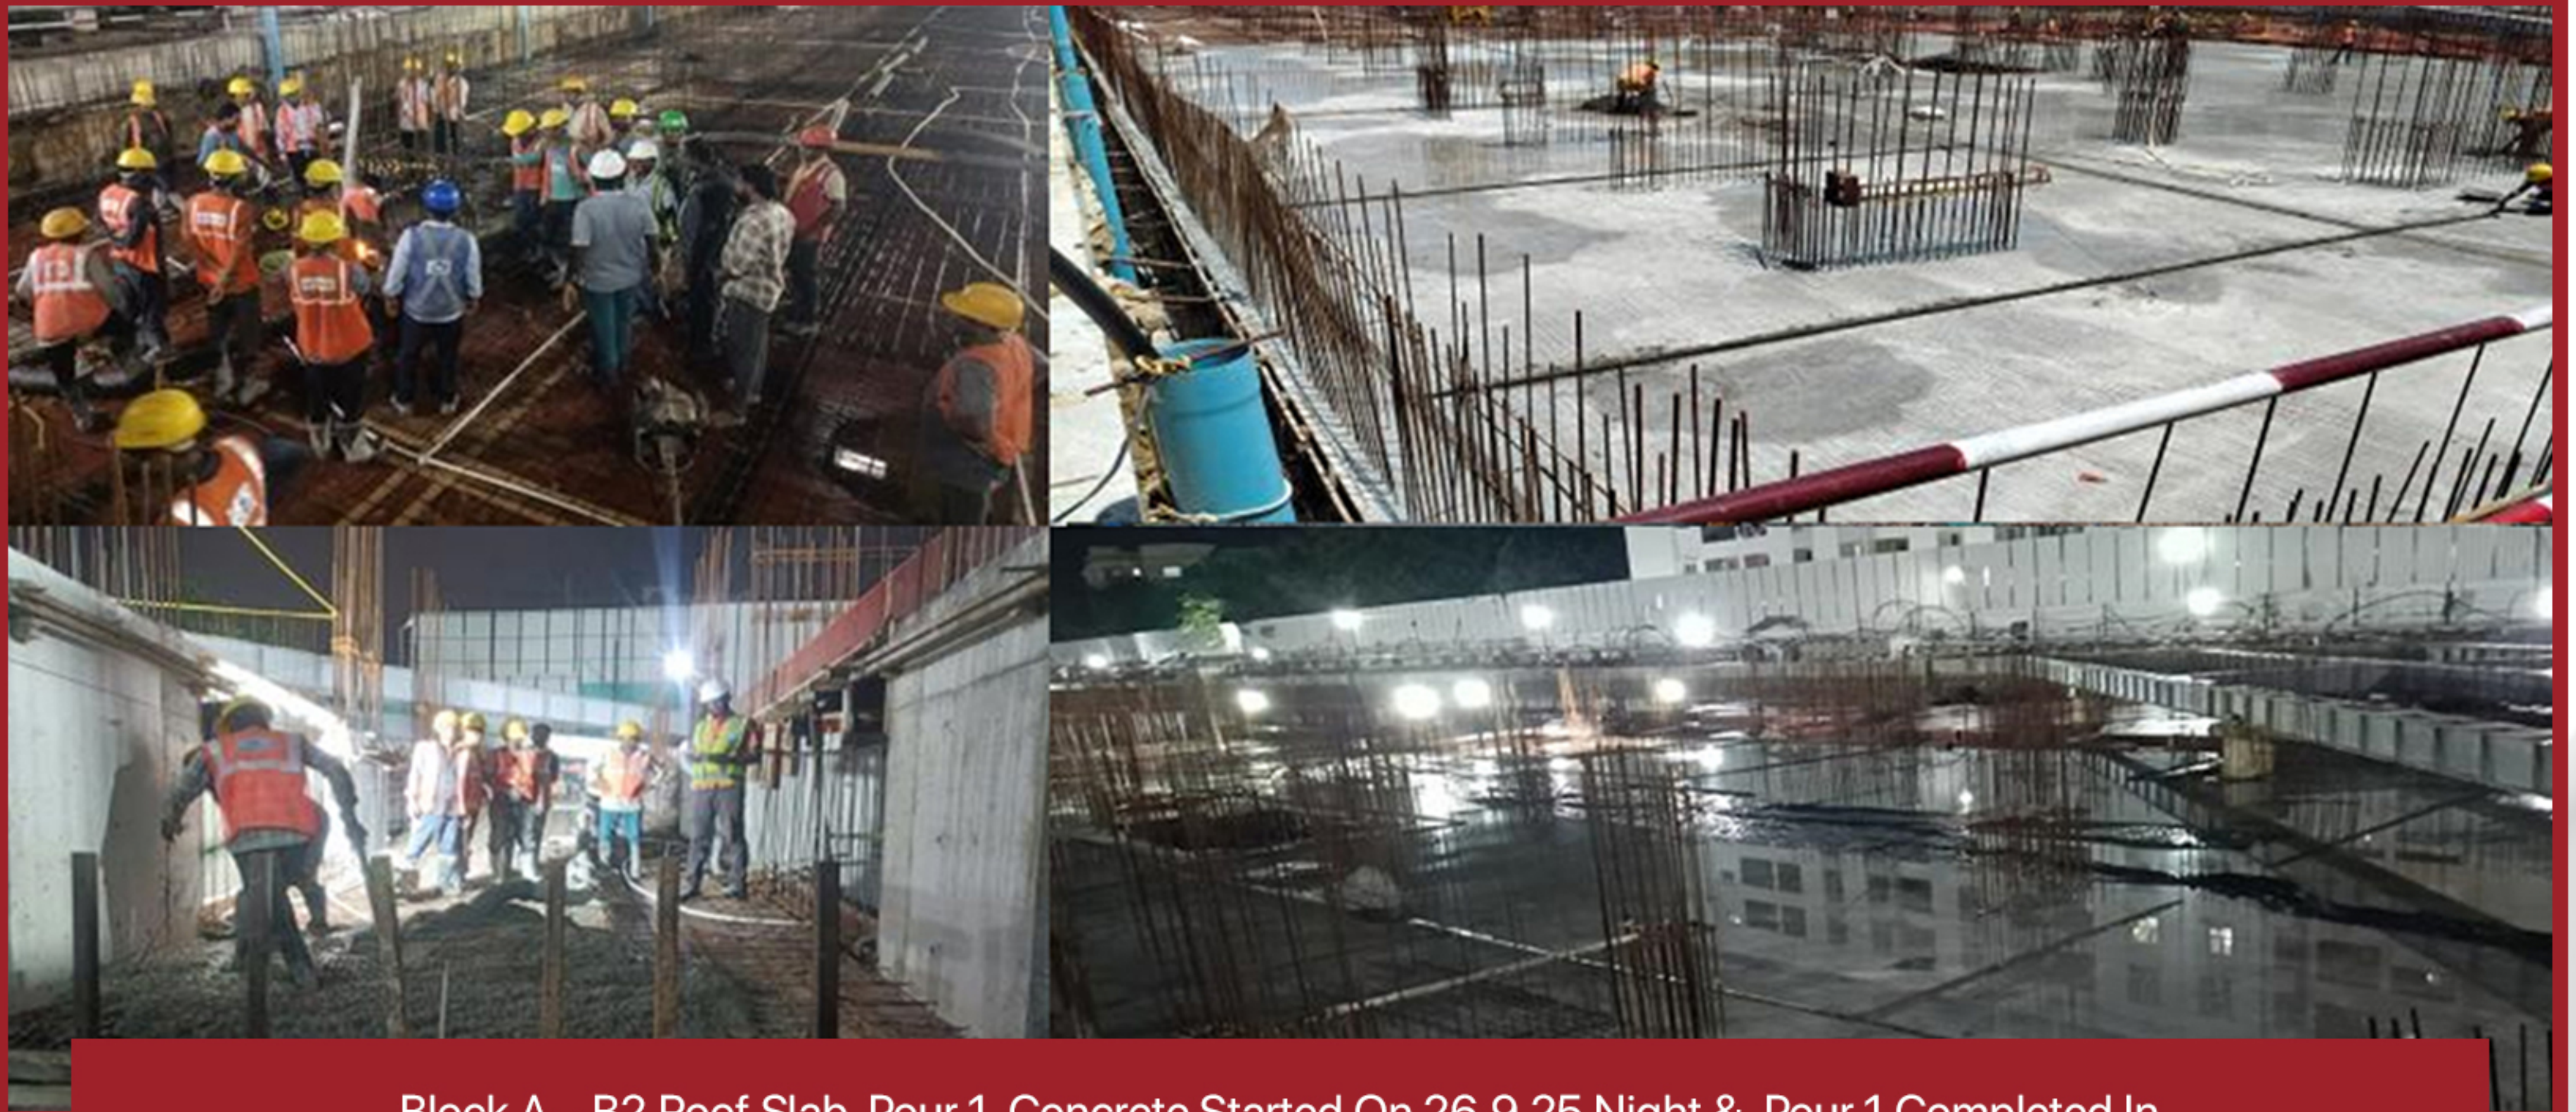

Block A – B2 Roof Slab Pour 1 Concrete Started On 26.9.25 Night & Pour 1 Completed In
2 Part Including Ramp 1 Concrete On 28.9.25 Morning Total 259 Cum At South West And South Side



Block B – Raft Rcc Part 1 / Se Side Completed / Retaining Wall & Column Wip

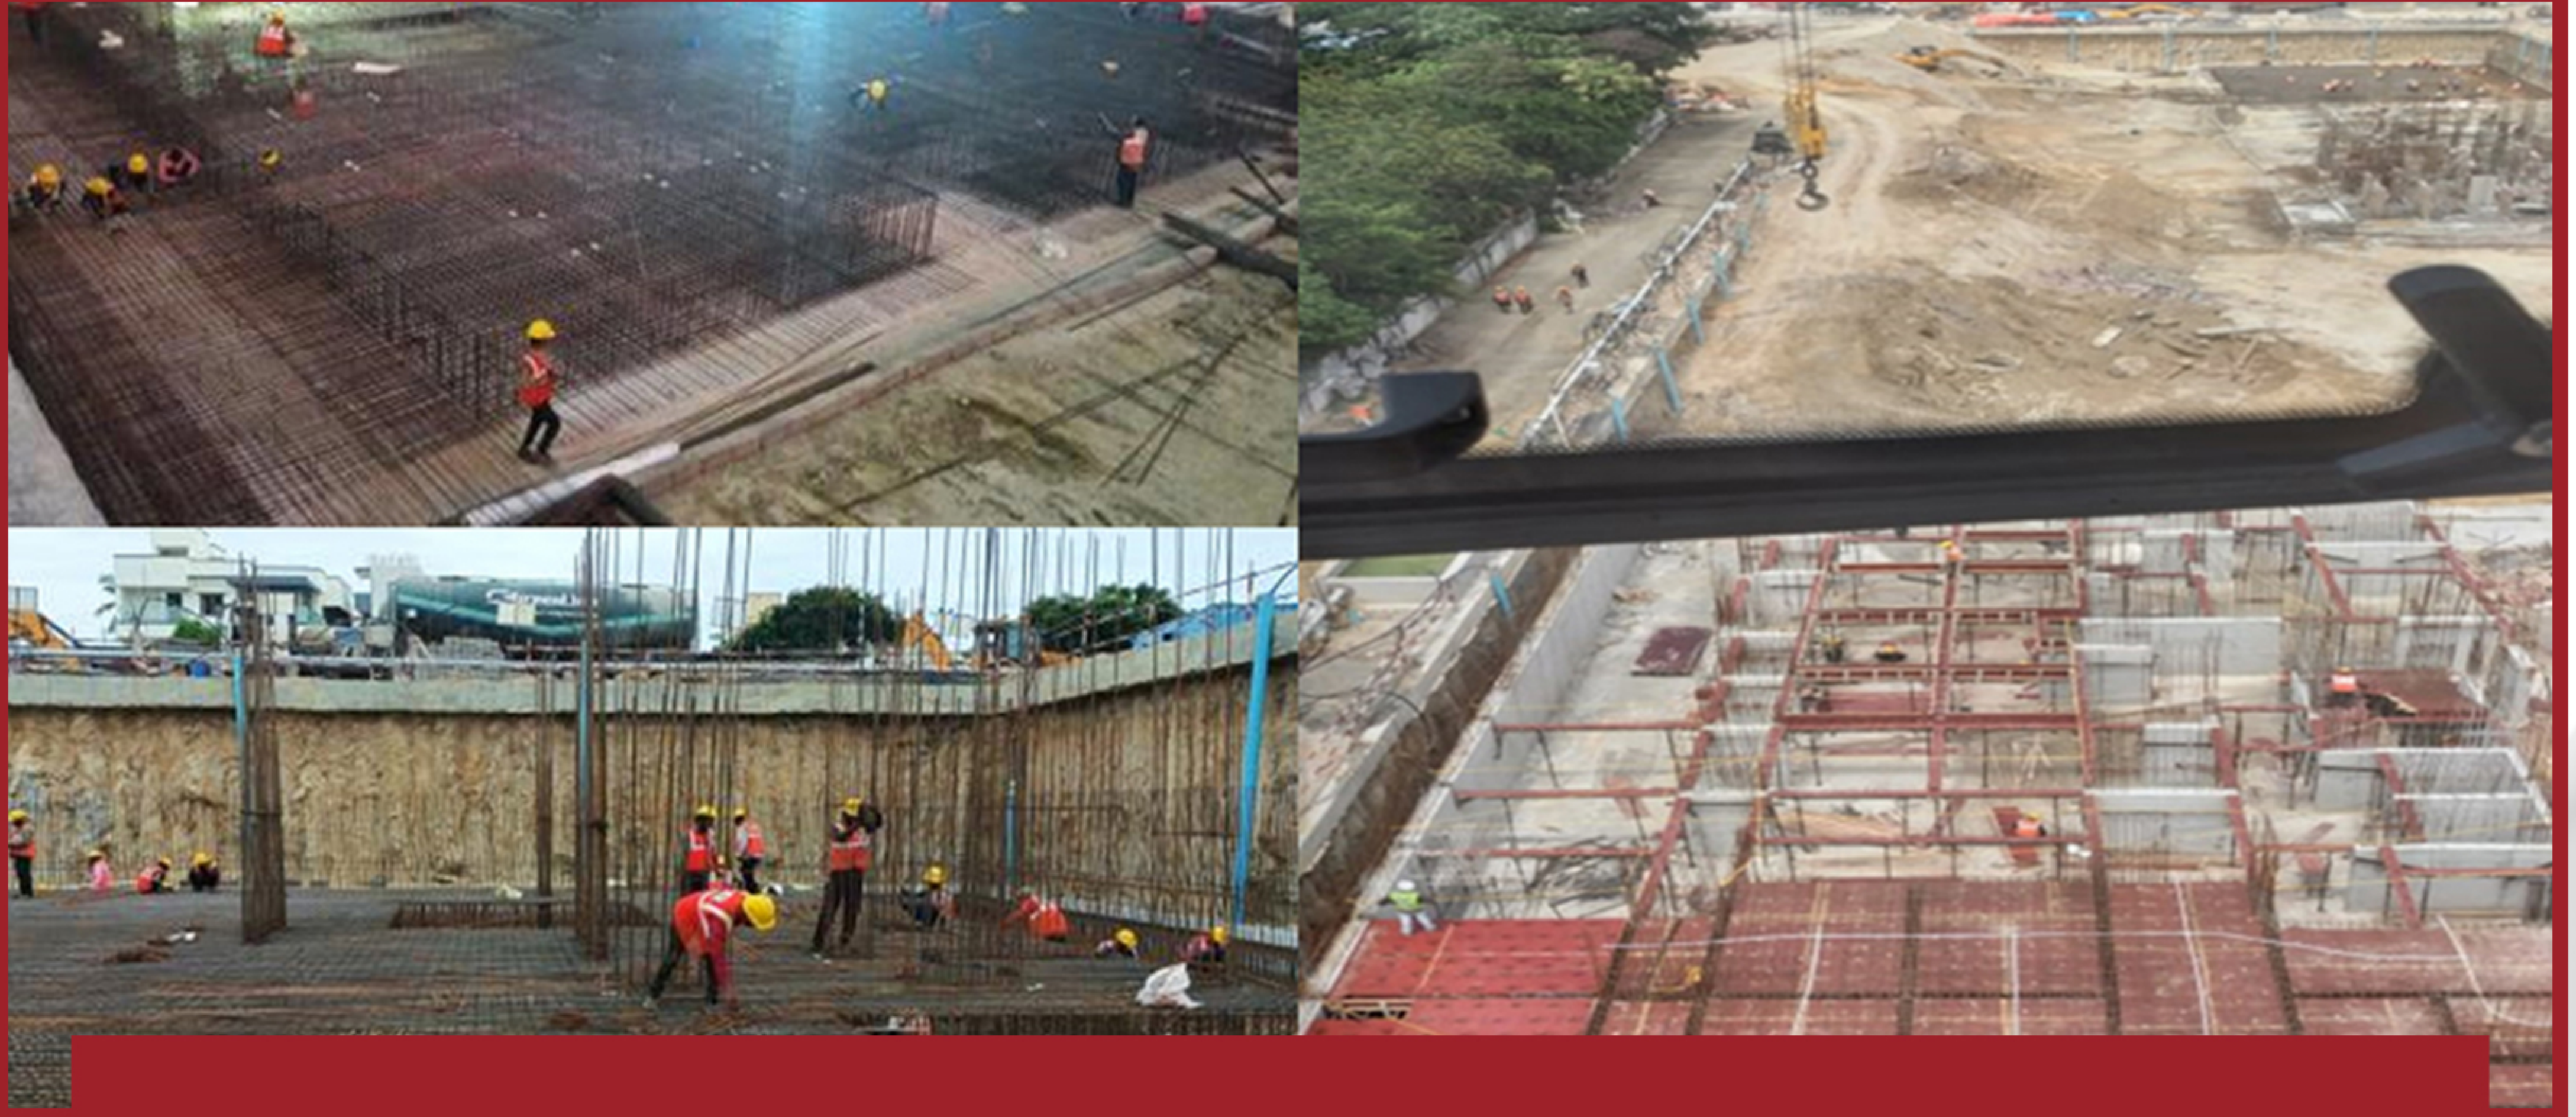

Block B – Raft Part 2 Reinforcement Works (Concrete Plan 29.9.25 / 640cum) And Part 3 Excavation



Club house area excavation works in progress
